


# LEGACY AT JONES FARM PHASE 2

FOR  
RBJ BAILEY, LLC  
PO BOX 2545  
HUNTSVILLE, AL 35804

JANUARY 2018

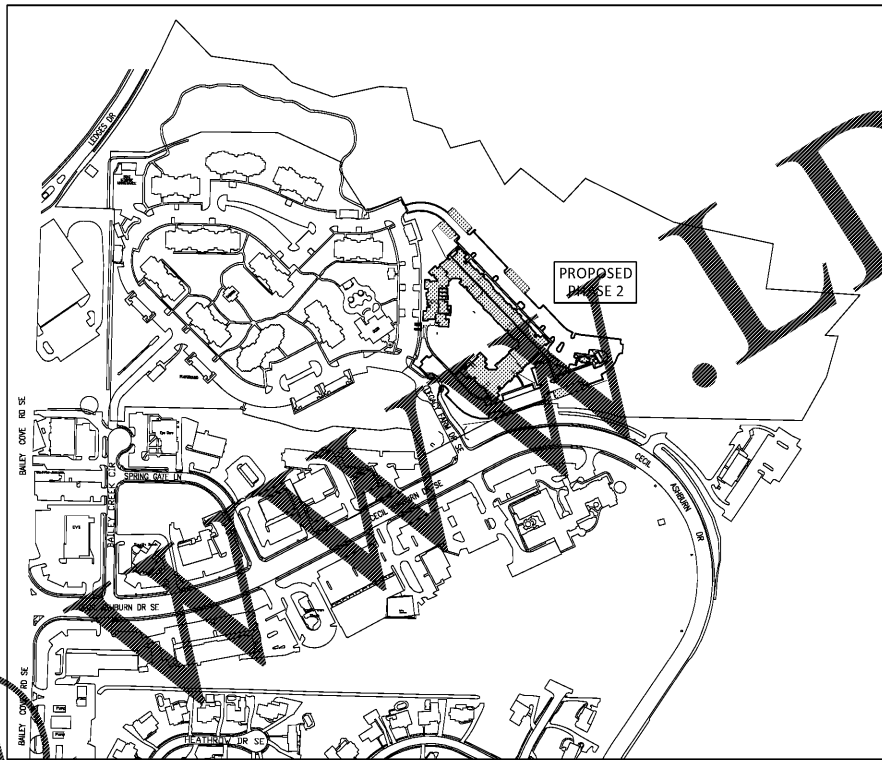

### EROSION AND SEDIMENT CONTROL CONSTRUCTION SEQUENCE

- ADEM EROSION AND SEDIMENT CONTROL HANDBOOK, 4TH EDITION.
- (This construction sequence is based on the engineer's opinion and not intended to be a comprehensive list of events and the contractor should use his/her discretion to determine the best sequence of construction. However, all erosion and sediment control measures must be installed in a timely fashion to perform properly.)
1. Install construction entrance with crushed aggregate base course. Entrance should be periodically cleaned to keep debris and mud from being carried onto existing roads. The existing drainageways should remain open until proposed storm system is functioning properly.
  2. Grade the property according to the grading plan, but leave all existing drainageways in place.
  3. Contractor should utilize water trucks, etc. to keep moisture content of subgrade at optimum level to reduce dust from construction traffic and improve compaction results.
  5. Maintain all erosion and sediment control measures, such that they are performing their function properly. Clean out sediment build-up when facilities reach 50% capacity. Wash down construction entrance periodically and make sure that adequate drainage is provided to reduce runoff onto existing roads.
  7. Contractor should be aware that erosion may occur in areas that are unprotected on the construction site. If the contractor observes sediment accumulation or erosion problems on site, then the contractor should take the necessary measures to stop sedimentation, such as silt fences, straw bale dams, etc., and then take the necessary measures to stop the erosion, such as seed/mulch, sod, erosion blankets, etc..
  10. When site construction is completed, remove all silt fences and gravel bag filters. Spread and grade collected materials on site.

### SITE UTILITY NOTES

1. ALL FILL MATERIAL IS TO BE IN PLACE, AND COMPACTED BEFORE INSTALLATION OF PROPOSED UTILITIES.
2. CONTRACTOR SHALL NOTIFY THE UTILITY AUTHORITIES INSPECTORS 72 HOURS BEFORE CONNECTING TO ANY EXISTING LINE.
3. SANITARY SEWER PIPE SHALL BE AS FOLLOWS:  
8" PVC SORBE PER ASTM D 3034, FOR PIPES LESS THAN 12' DEEP  
8" PVC SORBE PER ASTM D 3034, FOR PIPES MORE THAN 12' DEEP  
4" PVC SCHEDULE 40  
DUCTILE IRON PIPE PER ASTM C150
4. WATER LINES SHALL BE AS FOLLOWS:  
A. PIPE SIZES LESS THAN 3-INCHES THAT ARE INSTALLED BELOW GRADE AND OUTSIDE BUILDING SHALL COMPLY WITH ONE OR A COMBINATION OF THE FOLLOWING:  
1. SEAMLESS COPPER TUBING - TYPE "K" SOFT COPPER, ASTM B 88.  
A. FITTINGS: WROUGHT COPPER (LESS THAN ANGLEWELD JOINT), ASTM B 16.22.  
2. POLYVINYL CHLORIDE (PVC) WATER PIPE - PIPE, ASTM D 2511, WITH SDI 21 RATING, CONTINUALLY MARKED WITH MANUFACTURER'S NAME, PIPE SIZE, CELL CLASSIFICATION, SDI RATING, AND ASTM D 1784 MATERIAL CLASSIFICATION.  
A. PIPE JOINTS: INTERNALLY MOLDED BELL ENDS, ASTM D 2672.  
B. CEMENT PRIMER - ASTM - F908.  
C. SOLVENT CEMENT - ASTM - D 2554.  
B. PIPE SIZES 3-INCHES TO 4-INCHES THAT ARE INSTALLED BELOW GRADE AND OUTSIDE BUILDING SHALL COMPLY WITH ONE OR A COMBINATION OF THE FOLLOWING:  
1. DUCTILE IRON WATER PIPE, ANMA C151, THICKNESS CLASS 50.  
A. FITTINGS: OTHER MECHANICAL JOINT OR PUSH-ON JOINT, ANMA C110 OR ANMA C111.  
B. ELASTOMER GASKETS AND LUBRICANT: ASTM - F477.  
2. POLYVINYL CHLORIDE (PVC) WATER PIPE - PIPE, ANMA C900, RATED DR 18 (CLASS 150), CONTINUALLY MARKED AS REQUIRED.  
A. ELASTOMER GASKETS AND LUBRICANT: ASTM - F477 FOR SMALLER PIPES.  
B. PIPE JOINTS: INTERNALLY MOLDED BELL ENDS, ASTM D 3139.  
C. PIPE SIZES 4-INCHES AND LARGER THAT ARE INSTALLED BELOW GRADE AND OUTSIDE BUILDING SHALL COMPLY WITH THE FOLLOWING:  
1. DUCTILE IRON WATER PIPE, ANMA C151, THICKNESS CLASS 50.  
A. FITTINGS: OTHER MECHANICAL JOINT OR PUSH-ON JOINT, ANMA C110 OR ANMA C111.  
B. ELASTOMER GASKETS AND LUBRICANT: ASTM - F477.
5. MINIMUM TRENCH WIDTH SHALL BE 7 FEET.
6. ALL WATER JOINTS ARE TO BE MECHANICAL JOINTS WITH THRUST BLOCKING AS CALLED OUT IN SPECIFICATIONS.
7. ALL UTILITIES SHOULD BE KEPT TEN (10') APART (PARALLEL) OR WHEN CROSSING 18" APART (OUTSIDE EDGE OF PIPE TO OUTSIDE EDGE OF PIPE).
8. CONTRACTOR SHALL MAINTAIN A MINIMUM OF 4" OF COVER ON ALL WATERLINES.
9. IN THE EVENT OF A VERTICAL CONFLICT BETWEEN WATERLINES, SANITARY LINES, STORM LINES AND GAS LINES (EXISTING AND PROPOSED), THE SANITARY LINE SHALL BE DUCTILE IRON PIPE WITH MECHANICAL JOINTS AT LEAST TO FEET ON BOTH SIDES OF CROSSING. THE WATERLINE SHALL HAVE MECHANICAL JOINTS WITH APPROPRIATE THRUST BLOCKING AS REQUIRED TO PROVIDE A MINIMUM OF 18" CLEARANCE MEETING REQUIREMENTS OF ANMA C900 OR 21" (ANMA C-151) (CLASS 50). LINES UNDERGROUND SHALL BE INSTALLED, INSPECTED AND APPROVED BEFORE BACKFILLING.
10. TOPS OF EXISTING MANHOLES SHALL BE RAISED AS NECESSARY TO BE FLUSH WITH PROPOSED ELEVATIONS, AND TO BE ONE FOOT ABOVE FINISHED GROUND ELEVATIONS WITH WATER TIGHT LIDS.
12. ALL CONCRETE FOR ENCASUREMENTS SHALL HAVE A MINIMUM 28 DAY COMPRESSION STRENGTH AT 3000 P.S.I.
13. DRAWINGS DO NOT PURPORT TO SHOW ALL EXISTING UTILITIES.
14. EXISTING UTILITIES SHALL BE IDENTIFIED IN FIELD PRIOR TO INSTALLATION OF ANY NEW LINES.
15. REFER TO INTERIOR PLUMBING DRAWINGS FOR TIE-IN OF ALL UTILITIES.
16. CONTRACTOR IS RESPONSIBLE FOR COMPLYING TO THE SPECIFICATIONS OF THE LOCAL AUTHORITIES WITH REGARDS TO MATERIALS AND INSTALLATION OF THE WATER AND SEWER LINES.
17. ALL NECESSARY INSPECTIONS AND/OR CERTIFICATIONS REQUIRED BY CODE AND/OR UTILITY SERVICE COMPANIES SHALL BE PERFORMED PRIOR TO ANNOUNCED BUILDING POSSESSION AND THE FINAL CONNECTION OF SERVICE.
18. CONTRACTOR SHALL COORDINATE WITH ALL UTILITY COMPANIES FOR INSTALLATION REQUIREMENTS AND SPECIFICATIONS.
19. CONTRACTOR TO PROVIDE TRENCHING, CONDUIT, PULL WIRE AND BACKFILL FOR TELEPHONE AND ELECTRIC LINES.
20. THE CONTRACTOR IS RESPONSIBLE FOR FIELD VERIFYING THE EXACT LOCATION, DEPTH, AND MAKE OF ANY EXISTING WATER OR SEWER FACILITY PROPOSED FOR CONNECTION OR TIE-IN THIS PRIOR TO THE RELOCATION OF ANY WATER/GAS FACILITY REQUIRED TO AVOID ANY LINES.
21. ALL CONSTRUCTION TO APPLICABLE CITY/COUNTY SPECIFICATIONS AND ALL ORDINANCES IN CONFORMANCE WITH CITY/COUNTY ORDINANCES.
22. TRENCHES OF 20 FEET OR GREATER REQUIRE SHORING. SHORING DESIGN TO BE CERTIFIED BY A PROFESSIONAL ENGINEER. TRENCH SAFETY REQUIREMENTS WILL BE STRICTLY ENFORCED. CONTRACTOR TO MEET OR EXCEED ALL OSHA STANDARDS.
23. REFER TO ARCHITECTURAL PLANS FOR SITE LIGHTING AND ELECTRICAL PLANS.

### NOTICE TO GENERAL CONTRACTOR REGARDING UTILITY INSTALLATION.

THE INFORMATION SHOWN ON THESE PLANS RELATED TO THE EXISTING SUBSURFACE UTILITY LINES IS BASED ON FIELD SURVEY AND IS CORRECT TO THE BEST KNOWLEDGE OF THE ENGINEER. HOWEVER, THE EXISTING UTILITIES HAVE NOT BEEN EXPOSED AND VERIFIED. THEREFORE, THE CONTRACTOR SHALL BE RESPONSIBLE FOR FIELD VERIFYING THE EXACT LOCATION, DEPTH, AND MAKE OF ANY EXISTING WATER OR SEWER FACILITY PROPOSED FOR CONNECTION OR TIE-IN THIS PRIOR TO THE RELOCATION OF ANY WATER/GAS FACILITY REQUIRED TO AVOID ANY LINES. THE CONTRACTOR SHALL COORDINATE WITH ALL UTILITY COMPANIES FOR INSTALLATION REQUIREMENTS AND SPECIFICATIONS. THE CONTRACTOR SHALL COORDINATE WITH ALL UTILITY COMPANIES FOR INSTALLATION REQUIREMENTS AND SPECIFICATIONS. THE CONTRACTOR SHALL COORDINATE WITH ALL UTILITY COMPANIES FOR INSTALLATION REQUIREMENTS AND SPECIFICATIONS. THE CONTRACTOR SHALL COORDINATE WITH ALL UTILITY COMPANIES FOR INSTALLATION REQUIREMENTS AND SPECIFICATIONS.

### GENERAL PROJECT NOTES

- 1) CONTRACTOR SHALL DETERMINE THE EXACT LOCATION OF ALL EXISTING UTILITIES BEFORE COMMENCING WORK. HE AGREES TO BE FULLY RESPONSIBLE FOR ANY AND ALL DAMAGES WHICH MIGHT OCCUR BY HIS FAILURE TO EXACTLY LOCATE AND PRESERVE ANY AND ALL UTILITIES.
- 2) CONTRACTOR SHALL PREVENT THE DESTRUCTION OF SURVEY MONUMENTS, BENCH MARKS, PROPERTY CORNERS, AND ALL OTHER SURVEY POINTS. WHERE THE REMOVAL OF SUCH POINTS ARE NECESSARY FOR THE ACCOMPLISHMENT OF WORK, CONTRACTOR IS TO INFORM THE ENGINEER IN WRITING, PRIOR TO THE DISTURBANCE, AND IS NOT TO DISTURB THE POINT UNTIL WRITTEN PERMISSION TO DO SO HAS BEEN ISSUED BY THE ENGINEER.
- 3) ALL EXISTING TREES OUTSIDE THE CLEARING LIMITS ARE TO BE PROTECTED AND DAMAGED DURING THE DURATION OF THE PROJECT.
- 4) CONTRACTOR SHALL REPAIR ANY DAMAGE TO THE EXISTING STREETS THAT ARE A RESULT OF THE CONSTRUCTION ACTIVITIES.
- 5) ALL BOUNDERS, DEBRIS, EXCESS CONSTRUCTION MATERIALS, MATERIAL GENERATED FROM DEMOLITION OF EXISTING STRUCTURES, EXCAVATION FROM SITE GRADING AND/OR TRUCKS OR TRASH SHALL BE REMOVED FROM THE SITE AT THE CONTRACTOR'S EXPENSE.
- 6) CONTRACTOR SHALL BE RESPONSIBLE FOR HAVING EXISTING UTILITIES LOCATED PRIOR TO WORK. ENGINEER ASSUMES NO LIABILITY FOR THE ACCURACY OR COMPLETENESS OF UTILITIES DEPICTED ON THESE DRAWINGS.
- 7) PHOTOGRAPHS SHALL BE OBTAINED WHEN MATERIAL IN KIND TO THAT REMOVED.
- 8) ACCORDING TO THE ACCEPTED CONSTRUCTION PRACTICES, THE CONTRACTOR WILL BE SOLELY RESPONSIBLE FOR CONDITIONS ON THE JOBSITE, INCLUDING ALL SAFETY MATTERS AND PROPERTY DURING THE PERFORMANCE OF THE WORK. THE REQUIREMENTS WILL APPLY CONTINUOUSLY AND NOT BE LIMITED TO NORMAL WORKING HOURS.
- 9) CONTRACTOR SHALL PROVIDE ADEQUATE TRAFFIC CONTROL DEVICES AND SAFETY SIGNALS FOR CONSTRUCTION WORK WITHIN PUBLIC RIGHT-OF-WAYS IN ACCORDANCE WITH THE MANUA MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES FOR STREETS AND HIGHWAYS.
- 10) THE ENGINEER IS NOT RESPONSIBLE FOR REVIEW OF THE CONTRACTOR'S CONSTRUCTION PERFORMANCE OR SAFETY MEASURES IN OR AROUND THE JOBSITE.
- 11) NO CHANGES SHALL BE MADE TO THESE PLANS WITHOUT THE ENGINEER OF RECORD BEING NOTIFIED BEFORE CHANGES ARE MADE.
- 12) NO FILL DIRT SHALL BE PLACED ON THE PROPERTY THAT MIGHT INTERFERE WITH DRAINAGE FLOW FROM ADJACENT PROPERTY. STORM DRAINAGE SYSTEM SHALL BE INSTALLED PRIOR TO FILL MATERIAL BEING PLACED.
- 13) CONTRACTOR WILL BE RESPONSIBLE FOR CLEANING DIRT AND DEBRIS FROM ADJACENT PROPERTY, EXISTING STREETS, AND NEWLY CONSTRUCTED STORM DRAIN BOXES AND PIPES DURING CONSTRUCTION AS NEEDED. ANY DAMAGE TO ADJACENT LANDOWNERS WILL BE REPAIRED AT CONTRACTORS EXPENSE.
- 14) SITE AERIAL PHOTO AND OTHER TOPOGRAPHIC DATA SHOWN ON THE PLANS OR INCLUDED IN THE SPECIFICATIONS ARE FOR THE INFORMATION OF THE CONTRACTOR. THE CONTRACTOR SHALL MAKE SUCH ADDITIONAL INVESTIGATIONS AS REQUIRED TO ACQUAINT HIMSELF ADEQUATELY WITH THE SITE TOPOGRAPHY, AND THE SUBSURFACE SOIL CONDITIONS FOR PREPARATION OF HIS BID, AND FOR THE SUCCESSFUL EXECUTION OF THE WORK.
- 15) THE CONTRACTOR IS TO BE SOLELY RESPONSIBLE FOR THE PROTECTION OF HIS WORK. THE OWNER/ENGINEER MAY DIRECT THE CONTRACTOR TO PERFORM NECESSARY GRADING AND DRAINAGE TO PREVENT SURFACE RUNOFF FROM DAMAGING THE WORK OR ADJACENT PROPERTY.
- 16) CONTRACTOR SHALL BE REQUIRED TO INSTALL EROSION CONTROL MEASURES PRIOR TO COMMENCING WORK TO PREVENT LOOSE DIRT AND DEBRIS FROM WASHING ONTO STREETS AND ADJACENT PROPERTY. CONTRACTOR IS RESPONSIBLE FOR EROSION AND SEDIMENT CONTROL UNTIL THE FINAL INSPECTION BY THE ENGINEER.

### GRADING NOTES

- 1) THE CONTRACTOR IS CAUTIONED THAT THE LOCATION AND/OR ELEVATION OF EXISTING UTILITIES AS SHOWN ON THESE PLANS ARE BASED ON RECORDS OF VARIOUS UTILITY COMPANIES AND WHERE POSSIBLE MEASUREMENTS TAKEN IN THE FIELD. THE INFORMATION IS NOT TO BE RELIED ON AS BEING EXACT OR COMPLETE. THE CONTRACTOR MUST CALL THE APPROPRIATE UTILITY COMPANY AT LEAST 72 HOURS BEFORE ANY EXCAVATION TO REQUEST EXACT FIELD LOCATION OF UTILITY. IT SHALL BE THE RESPONSIBILITY OF THE CONTRACTOR TO RELOCATE ALL EXISTING UTILITIES WHICH CONFLICT WITH THE PROPOSED IMPROVEMENTS SHOWN ON THE PLANS.
- 2) ALL CUT OR FILL SLOPES SHALL BE 3:1 OR FLATTER UNLESS OTHERWISE NOTED.
- 3) EXISTING PIPES SHALL BE CLEANED OUT TO REMOVE ALL SILT AND DEBRIS AS NEEDED OR DIRECTED BY ENGINEER DURING AND AFTER CONSTRUCTION.
- 4) EXISTING AND PROPOSED GRADE CONTOUR INTERVALS SHOWN AT 1 FOOT.
- 5) CONTRACTOR SHALL ADJUST AND/OR CUT EXISTING PAVEMENT AS NECESSARY TO ASSURE A SMOOTH FIT AND CONTINUOUS GRADE.
- 6) CONTRACTOR SHALL ASSURE POSITIVE DRAINAGE AWAY FROM ANY PROPOSED OR EXISTING BUILDINGS FOR ALL NATURAL AND PAVED AREAS.
- 7) CONSTRUCTION SHALL COMPLY WITH ALL APPLICABLE GOVERNING AUTHORITIES AND BE CONSTRUCTED IN ACCORDANCE WITH THE LATEST CODES.
- 8) GEOTECHNICAL REPORT BY GEOSOLUTIONS, LLC SHALL BE MADE A PART OF THESE PLANS AND SHALL OVER-RIDE ANY CONFLICTING INFORMATION FOUND WITHIN.
- 9) COMPACTED PAD SHALL BE MINIMUM 95% STANDARD PROCTOR DENSITY AT OR ABOUT MOISTURE CONTENT. PAD SHALL BE CONSTRUCTED OF STRUCTURAL FILL PLACED IN COMPACTED LIFTS GEOTECHNICAL REPORT.
- 10) REMOVAL OF ALL UNSUITABLE MATERIALS BELOW THE GROUND SLAB AND WITHIN A ROUGHLY TRIANGULAR AREA WITHIN THE LIMITS OF A 1:1 PROJECTION DOWN AND OUT FROM THE EDGES OF THE FOUNDATION, OR AS DIRECTED BY THE GEOTECHNICAL REPORT.
- 11) STRUCTURAL FILL SHALL BE CLEAN, SELECT FILL FREE OF FOREIGN MATTER IN UNIFORM, LOOSE HORIZONTAL LAYERS 8 INCHES IN DEPTH AND COMPACTED TO A MINIMUM OF 95% STANDARD PROCTOR DENSITY AT OR ABOVE MOISTURE CONTENT, OR AS DIRECTED BY THE GEOTECHNICAL REPORT.
- 12) STRUCTURAL FILL SHALL EXTEND A MINIMUM OF 10 FEET BEYOND THE OUTSIDE FACE OF THE BUILDING SHELL, OR AS DIRECTED BY THE GEOTECHNICAL ENGINEER.
- 13) ALL ABANDONED FOOTINGS, FOUNDATIONS, AND UTILITY PIPING (GREATER THAN 12" DIA) FOUND BENEATH THE PROPOSED BUILDINGS SHALL BE REMOVED AND BACKFILLED PER GEOTECHNICAL RECOMMENDATIONS. EXISTING FOOTINGS AND FOUNDATIONS IN THE PARKING AREAS MAY BE LEFT IN PLACE AT DEPTHS GREATER THAN 2' BELOW FINISHED SOIL SURFACE. UTILITIES (SMALLER THAN 12" DIA) FOUND IN THE PARKING AREAS MAY REMAIN IF LOCATED 2' OR MORE BELOW FINISHED SOIL SUBGRADE.
- 14) ALL BUILDING PADS WILL BE CERTIFIED BY THE GEOTECHNICAL ENGINEER FOR COMPACTION, STABILIZATION, AND MOISTURE CONTENT, AND THAT SOIL CONDITIONS BENEATH THE BUILDING SHELL MEETS OR EXCEEDS SPECIFICATIONS FOUND IN THE CONTRACT DOCUMENTS (PLANS, SPECIFICATIONS, GEOTECHNICAL REPORT, ETC).
- 15) FARTH FILL SHALL BE PLACED IN UNIFORM LAYERS OR LIFTS NOT EXCEEDING 6" COMPACTED THICKNESS.
- 16) ALL FILL MATERIAL OUTSIDE PAVED AREAS SHALL BE COMPACTED TO 95% OF THE MAXIMUM DRY DENSITY, PLUS OR MINUS 2% OF OPTIMUM MOISTURE CONTENT, ASTM D-6708.
- 17) ALL EARTHWORK SHALL BE MONITORED BY A REGISTERED GEOTECHNICAL ENGINEER.

### INDEX TO SHEETS

COVER SHEET AND PROJECT NOTES	C1.1
OVERALL LAYOUT AND GENERAL PLAN	C2.1
LAYOUT AND PAVING PLAN	C2.2 TO C2.4
OVERALL GRADING AND DRAINAGE PLAN	C3.1
GRADING AND DRAINAGE PLAN - STORM	C3.2 TO C3.4
GRADING AND DRAINAGE PLAN - DETAILED GRADING	C3.5 TO C3.7
EROSION AND SEDIMENT CONTROL	C4.1 TO C4.3
WATER AND SEWER PLAN	C5.1 TO C5.3
SEWER PROFILES	C5.4
CONSTRUCTION DETAILS	C6.1 TO C6.6
LANDSCAPE PLAN	L1
LANDSCAPE DETAILS	L2

### TELEPHONE COMPANY

THE Engineering Dept HAS REVIEWED THE REQUIRED SUBMISSION MATERIAL FOR THE PROPOSED SUBDIVISION IN SUFFICIENT DETAIL TO DETERMINE THAT SERVICE CAN BE MADE AVAILABLE. WHEN IMPROVEMENTS ARE COMPLETED, "AS BUILT" CONSTRUCTION PLANS WILL BE SUBMITTED TO THE HUNTSVILLE ENGINEERING DEPARTMENT.

1-10-18  
DATE  
Drew S Short OSPG  
NAME AND TITLE  
A.T.&T.

### CABLE COMPANY

THE Engineering Dept HAS REVIEWED THE REQUIRED SUBMISSION MATERIAL FOR THE PROPOSED SUBDIVISION IN SUFFICIENT DETAIL TO DETERMINE THAT SERVICE CAN BE MADE AVAILABLE. WHEN IMPROVEMENTS ARE COMPLETED, "AS BUILT" CONSTRUCTION PLANS WILL BE SUBMITTED TO THE HUNTSVILLE ENGINEERING DEPARTMENT.

1/10/2018  
DATE  
NAME AND TITLE

### HUNTSVILLE UTILITIES ELECTRIC DEPARTMENT

THE Engineering Dept HAS REVIEWED THE REQUIRED SUBMISSION MATERIAL FOR THE PROPOSED SUBDIVISION IN SUFFICIENT DETAIL TO DETERMINE THAT SERVICE CAN BE MADE AVAILABLE. WHEN IMPROVEMENTS ARE COMPLETED, "AS BUILT" CONSTRUCTION PLANS WILL BE SUBMITTED TO THE HUNTSVILLE ENGINEERING DEPARTMENT.

1/10/18  
DATE  
Daron Hunter  
NAME AND TITLE  
ELECTRIC DEPARTMENT

### NATURAL GAS SERVICE


THE NATURAL GAS DEPARTMENT OF HUNTSVILLE HAS REVIEWED THE REQUIRED SUBMISSION MATERIAL FOR THE PROPOSED SUBDIVISION IN SUFFICIENT DETAIL TO DETERMINE THAT SERVICE (CAN OR CANNOT) BE MADE AVAILABLE. THE APPLICANT, AT THE PRESENT TIME, DOES NOT REQUEST NATURAL GAS SERVICE FOR THIS SUBDIVISION. THE NATURAL GAS DEPARTMENT RESERVES THE RIGHT TO CONSIDER GAS SERVICE FOR THIS SUBDIVISION IN THE FUTURE.

1/10/18  
DATE  
Dol Perry  
NAME AND TITLE  
MANAGER

### HUNTSVILLE UTILITIES WATER DEPARTMENT

THE Engineering Dept HAS REVIEWED THE REQUIRED SUBMISSION MATERIAL FOR THE PROPOSED SUBDIVISION IN SUFFICIENT DETAIL TO DETERMINE THAT SERVICE CAN BE MADE AVAILABLE. WHEN IMPROVEMENTS ARE COMPLETED, "AS BUILT" CONSTRUCTION PLANS WILL BE SUBMITTED TO THE HUNTSVILLE ENGINEERING DEPARTMENT.

1/10/2018  
DATE  
NAME AND TITLE  
WATER DEPARTMENT



**PRICE, P.C.**  
CONSULTING ENGINEERS

ALL DOCUMENTS PREPARED OR REVISED BY PRICE, P.C. SHALL BE MADE AVAILABLE TO THE CLIENT AND TO THE PUBLIC. THE CLIENT SHALL BE RESPONSIBLE FOR THE PROTECTION OF THESE DOCUMENTS. THE CLIENT SHALL BE RESPONSIBLE FOR THE PROTECTION OF THESE DOCUMENTS. THE CLIENT SHALL BE RESPONSIBLE FOR THE PROTECTION OF THESE DOCUMENTS.

LEGACY AT JONES FARM  
PHASE 2

CLIENT  
RBJ BAILEY, LLC  
PO BOX 2545  
HUNTSVILLE, AL  
35804

SITE ADDRESS  
1 LEGACY  
FARM DR SE  
HUNTSVILLE,  
AL 35802

REVISIONS

SHEET TITLE  
COVER SHEET

SCALE: NTS  
APPROVED BY: JRI  
PROJECT NO: 17-105  
DATE: 12/29/17  
SHEET NUMBER  
C1.1 OF C6.6
