

EROSION, SEDIMENTATION & POLLUTION CONTROL PLAN CHECKLIST
STAND ALONE CONSTRUCTION PROJECTS
SWCD - REGION II - GWINNETT COUNTY

Project Name: CHRISTIAN BROTHERS AUTOMOTIVE Address: 5650 PEACHTREE INDUSTRIAL BLVD
 City/County: NORCROSS/GWINNETT COUNTY Date on Plans: OCTOBER 16, 2018
 Name & email of person filling out checklist: Thomas Dugan, thomas.dugan@leccraweng.com

Plan Included
 Page # Y/N

TO BE SHOWN ON ES&PC PLAN

- The applicable Erosion, Sedimentation and Pollution Control Plan Checklist established by the Commission as of January 1 of the year in which the land-disturbing activity was permitted. (The completed Checklist must be submitted with the ES&PC Plan or the Plan will not be reviewed)
- Level II certification number issued by the Commission, signature and seal of the certified design professional. (Signature, seal and Level II number must be on each sheet pertaining to ES&PC plan or the Plan will not be reviewed)
- Limits of disturbance shall be no greater than 50 acres at any one time without prior written authorization from the EPD District Office. If EPD approves the request to disturb 50 acres or more at any one time, the plan must include at least 4 of the BMPs listed in Appendix 1 of this checklist. (A copy of the written approval by EPD must be attached to the plan for the plan to be reviewed.)
- The name and phone number of the 24-hour local contact responsible for erosion, sedimentation and pollution controls.
- Provide the name, address and phone number of primary permittee.
- Note total and disturbed acreage of the project or phase under construction.
- Provide the GPS location of the construction exit for the site. Give the Latitude and Longitude in decimal degrees.
- Initial date of the Plan and the dates of any revisions made to the Plan including the entity who requested the revisions.
- Description of the nature of construction activity.
- Provide vicinity map showing site's relation to surrounding areas. Include designation of specific phase, if necessary.
- Identify the project receiving waters and describe all sensitive adjacent areas including streams, lakes, residential areas, wetlands, marshlands, etc. which may be affected.
- Design professional's certification statement and signature that the site was visited prior to development of the ES&PC Plan as stated on page 15 of the permit.
- Design professional's certification statement and signature that the permittee's ES&PC Plan provides for an appropriate and comprehensive system of BMPs and sampling to meet permit requirements as stated on page 15 of the permit.
- Clearly note the statement that "The design professional who prepared the ES&PC Plan is to inspect the installation of the initial sediment storage requirements and perimeter control BMPs within 7 days after installation."
- Clearly note the statement that "Non-exempt activities shall not be conducted within the 25 or 50-foot undisturbed stream buffers as measured from the point of wasted vegetation or within 25-feet of the coastal marshland buffer as measured from the Jurisdictional Determination Line without first acquiring the necessary variances and permits."
- Provide a description of any buffer encroachments and indicate whether a buffer variance is required.
- Clearly note the statement that "Amendment/revisions to the ES&PC Plan which have a significant effect on BMPs with a hydraulic component must be certified by the design professional."
- Clearly note the statement that "Waste materials shall not be discharged to waters of the State, except as authorized by a section 404 permit."
- Clearly note statement that "The escape of sediment from the site shall be prevented by the installation of erosion and sediment control measures and practices prior to land disturbing activities."
- Clearly note statement that "Erosion control measures will be maintained at all times. If full implementation of the approved plan does not provide for effective erosion control, additional erosion and sediment control measures shall be implemented to control or treat the sediment source."
- Clearly note the statement "Any disturbed area left exposed for a period greater than 14 days shall be stabilized with mulch or temporary seeding."
- Any construction activity which discharges storm water into an Impaired Stream Segment, or within 1 linear mile upstream of land within the same watershed as, any portion of a Biologically Impaired Stream Segment must comply with Part III, C, of the Permit. Include the completed Appendix 1 listing all the BMPs that will be used for those areas of the site which discharge to the Impaired Stream Segment."
- If a TMDL Implementation Plan for sediment has been finalized for the Impaired Stream Segment (identified in item 22 above) at least six months prior to submittal of NOI, the ES&PC Plan must address any site-specific conditions or requirements included in the TMDL Implementation Plan."
- BMPs for concrete washdown of tools, concrete mixer chutes, hoppers and the rear of the vehicles. Washout of the drum at the construction site is prohibited.
- Provide BMPs for the remediation of all petroleum spills and leaks.
- Description of the measures that will be installed during the construction process to control pollutants in storm water that will occur after construction operations have been completed.
- Description of the practices that will be used to reduce the pollutants in storm water discharges."
- Description and chart or timeline of the intended sequence of major activities which disturb soils for the major portions of the site (i.e., initial perimeter and sediment storage BMPs, clearing and grubbing activities, excavation activities, utility activities, temporary and final stabilization).

C-2.3 Y

C-2.3 Y

C-2.3 Y

ALL Y

C-2.0 Y

C-2.3 Y

C-2.3 Y

C-2.3 Y

C-2.3 Y

N/A

C-2.3 Y

C-2.3 Y

C-2.3 Y

C-2.3 Y

C-2.3 Y

C-2.3 Y

N/A

C-2.3 Y

C-2.3 Y

C-2.3 Y

C-2.3 Y

C-2.3 Y

C-2.3 Y

- Provide complete requirements of inspections and record keeping by the primary permittee.
- Provide complete requirements of sampling frequency and reporting of sampling results.
- Provide complete details for retention of records as per Part IV.F. of the permit.
- Description of analytical methods to be used to collect and analyze the samples from each location.
- Appendix B rationale for NTU values at all outfall sampling points where applicable.
- Delineate all sampling locations, perennial and intermittent streams and other water bodies into which storm water is discharged.
- A description of appropriate controls and measures that will be implemented at the construction site including: (1) initial sediment storage requirements and perimeter control BMPs, (2) intermediate grading and drainage BMPs, and (3) final BMPs. For construction sites where there will be no mass grading and the initial perimeter control BMPs, intermediate grading and drainage BMPs, and final BMPs are the same, the plan may combine all of the BMPs into a single phase.
- Graphic scale and North arrow.
- Existing and proposed contour lines with contour lines drawn at an interval in accordance with the following:

Map Scale	Ground Slope	Contour Interval, ft
1 inch = 100ft or larger scale	Flat 0 - 2%	0.5 or 1
	Rolling 2 - 6%	1 or 2
	Steep 6% +	2.5 or 10
- Use of alternative BMPs whose performance has been documented to be equivalent to or superior to conventional BMPs as certified by a Design Professional (unless disapproved by EPD or the Georgia Soil and Water Conservation Commission). Please refer to the Alternative BMP Guidance Document found at www.gaswcc.org.
- Use of alternative BMP for application to the Equivalent BMP List. Please refer to Appendix A-2 of the Manual for Erosion & Sediment Control in Georgia 2016 Edition.
- Delineation of the applicable 25-foot or 50-foot undisturbed buffers adjacent to state waters and any additional buffers required by the Local Issuing Authority. Clearly note and delineate all areas of impact.
- Delineation of on-site wetlands and all state waters located on and within 200 feet of the project site.
- Delineation and acreage of contributing drainage basins on the project site.
- Provide hydrology study and maps of drainage basins for both the pre- and post-developed conditions.
- An estimate of the runoff coefficient or peak discharge flow of the site prior to and after construction activities are completed.
- Storm-drain pipe and weir velocities with appropriate outlet protection to accommodate discharges without erosion. Identify/delineate all storm water discharge points.
- Soil series for the project site and their delineation.
- The limits of disturbance for each phase of construction.
- Provide a minimum of 67 cubic yards of sediment storage per acre drained using a temporary sediment basin, retitled detention pond, and/or excavated inlet sediment traps for each common drainage location. Sediment storage volume must be in place prior to and during all land disturbance activities until final stabilization of the site has been achieved. A written justification explaining the decision to use equivalent controls when a sediment basin is not attainable must be included in the plan for each common drainage location in which a sediment basin is not provided. A written justification as to why 67 cubic yards of storage is not attainable must also be given. Worksheets from the Manual included for structural BMPs and all calculations used by the storage design professional to obtain the required sediment when using equivalent controls. When discharging from sediment basins and impoundments, permittees are required to utilize outlet structures that withdraw water from the surface, unless infeasible. If outlet structures that withdraw water from the surface are not feasible, a written justification explaining this decision must be included in the plan.
- Location of Best Management Practices that are consistent with and no less stringent than the Manual for Erosion and Sediment Control in Georgia. Use uniform coding symbols from the Manual, Chapter 4, with legend.
- Provide detailed drawings for all structural practices. Specifications, at a minimum, meet the guidelines for the Manual for Erosion and Sediment Control in Georgia.
- Provide vegetative plan, noting all temporary and permanent vegetative practices. Include species, planting dates and seeding, fertilizer, lime and mulching rates. Vegetative plan shall be site specific for appropriate time of the year that seeding will be done and for the appropriate geographic region of Georgia.

*If using this checklist for a project that is less than 1 acre and not part of a commercial development but within 200 ft of a perennial stream, some checklist items would be N/A. Effective January 1, 2018

C-2.0 Y

C-2.0-2.2 Y

C-2.0-2.2 Y

C-2.0-2.2 Y

C-2.0-2.2 Y

C-2.0-2.2 Y

C-2.4-2.6 Y

C-2.4-2.6 Y

Mix fertilizer into soil surface. Fertilize based on soil tests or Table 6-6.1.

Table 6-6.1 Fertilizer Requirements for Soil Surface Application

Fertilizer Type	Fertilizer Rate (lbs/acre)	Fertilizer Rate (lbs/sq ft)	Nitrogen	Phosphorus
10-10-10	1000	0.25	F	F



Agricultural lime should be applied based on soil tests or agronomic rates to 2 tons per acre.

Table 6-6.3 Fertilizer Requirements for Sod

Type of Species	Planting Year	Fertilizer (N-P-K)	Rate (lbs/acre)	Nitrogen Top Dressing Rate (lbs/acre)
cool season grasses	first	6-12-12	1500	50-100
	second	6-12-12	1000	30
warm season grasses	first	6-12-12	1500	50-100
	second	6-12-12	800	30

Table 6-6.2 Sod Planting Requirements

Grass	Varieties	Resource Area	Growing Season
Bermudagrass	Common Tifway Tifgreen Tifdwarf	M-L, P.C. P.C. P.C.	warm weather
Bahiagrass	Pensacola	P.C.	warm weather
Centipede	-	P.C.	warm weather
St. Augustine	Common Bitterblue Raleigh	C	warm weather
Zoysia	Emerald Myer	P.C.	warm weather
Tall Fescue	Kentucky	M-L, P	cool weather

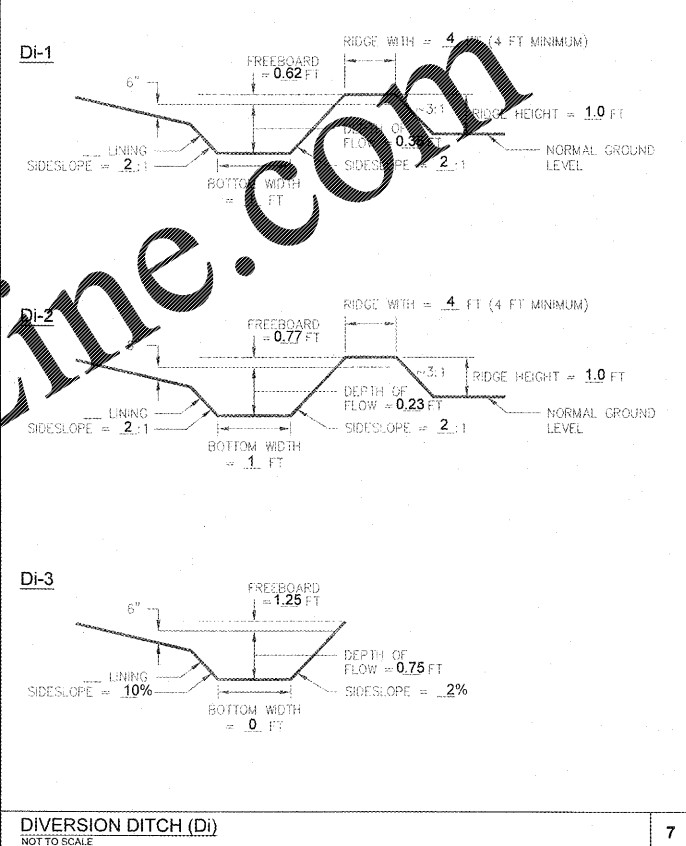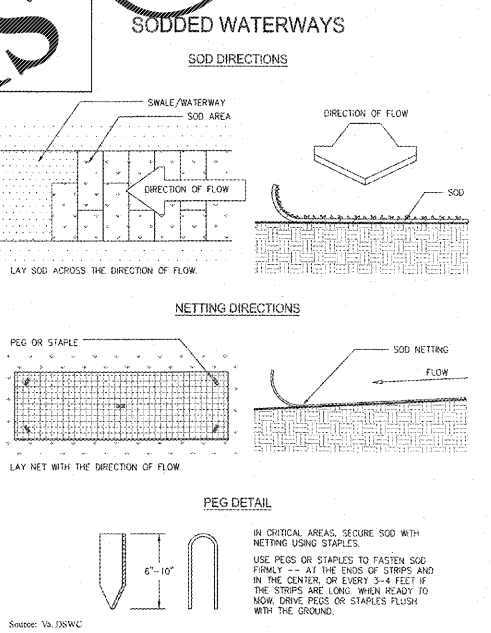

CERTIFICATION STATEMENT
 I CERTIFY THAT THE PERMITTEE'S EROSION, SEDIMENTATION AND POLLUTION CONTROL PLAN PROVIDES FOR AN APPROPRIATE AND COMPREHENSIVE SYSTEM OF BEST MANAGEMENT PRACTICES REQUIRED BY THE GEORGIA WATER QUALITY CONTROL ACT AND THE DOCUMENT 'MANUAL FOR EROSION AND SEDIMENT CONTROL IN GEORGIA' PUBLISHED BY THE STATE SOIL AND WATER CONSERVATION COMMISSION AS OF JANUARY 1 OF THE YEAR IN WHICH LAND-DISTURBING ACTIVITY WAS PERMITTED, PROVIDES FOR THE SAMPLING OF THE RECEIVING WATER(S) OR THE SAMPLING OF STORM WATER OUTFALLS AND THAT THE DESIGNED SYSTEM OF BEST MANAGEMENT PRACTICES AND SAMPLING METHODS IS EXPECTED TO MEET THE REQUIREMENTS CONTAINED IN THE GENERAL NPDES PERMIT NO. GAR 100001."

I CERTIFY UNDER PENALTY OF THE LAW THAT THIS PLAN WAS PREPARED AFTER A SITE VISIT TO THE LOCATIONS DESCRIBED HEREIN BY MYSELF OR MY AUTHORIZED AGENT, UNDER MY SUPERVISION."

UPON THE INSTALLATION OF THE PHASE 1 EROSION CONTROL MEASURES, I WILL VISIT THE SITE TO PERFORM THE INSPECTION CERTIFICATION WITHIN 7 DAYS, ONCE NOTIFIED BY THE CONTRACTOR.

12/20/18
 GEORGIA LICENSED PROFESSIONAL (SIGN)
 MARK S. LECRAW
 GEORGIA LICENSED PROFESSIONAL (PRINT)
 030828
 GEORGIA PEA
 000008928
 GEORGIA EROSION CONTROL LEVEL 2 CERTIFICATION 3
EROSION CONTROL CERTIFICATION
 NOT TO SCALE

Mark S. LeCraw
 Level II Certified Design Professional
 CERTIFICATION NUMBER 000008928
 ISSUED 03/11/2016 Expires 03/11/2021

DESIGN TEAM:
 DRAWN BY: TDD
 DESIGNED BY: TDD
 REVIEWED BY: MSL

811
 Know what's below.
 Call before you dig.

DETAILS ARE NOT DRAWN TO SCALE

JOB #: 188005
 DATE: 08/18/2018
 EROSION CONTROL DETAILS - 3

LECCRAW ENGINEERING, INC.
 3475 GAYLOR DRIVE, SUITE 100
 DULUTH, GA 30096
 PHONE - 770.548.9100
 FAX - 770.441.0208
 WWW.LECCRAWENGINEERING.COM
 PER000796

REV #	DATE	BY	DESCRIPTION
1		MSL	ISSUED FOR PERMIT
2		TDD	REVISED PER COMMENTS
3		MSL	REVISED PER COMMENTS

CLIENT
 CHRISTIAN BROTHERS AUTOMOTIVE
 17725 KATY FREEWAY - SUITE 200 - HOUSTON, TX 77084

PROJECT
 CHRISTIAN BROTHERS AUTOMOTIVE - NORCROSS
 5650 PEACHTREE INDUSTRIAL BLVD
 LAND LOT 272, DISTRICT 6, PARCEL 6272 327
 NORCROSS, GWINNETT COUNTY, GA

SEAL:

DESIGN TEAM:
 DRAWN BY: TDD
 DESIGNED BY: TDD
 REVIEWED BY: MSL

811
 Know what's below.
 Call before you dig.

DETAILS ARE NOT DRAWN TO SCALE

JOB #: 188005
 DATE: 08/18/2018
 EROSION CONTROL DETAILS - 3

Drawing name: L:\188005 - Christian Brothers Automotive - Norcross_GA\CADD\CONSTR\188005-05_ES&PC DETAILS.dwg EROSION CONTROL DETAILS - 3 Dec 18, 2018 9:42am by: thomas.dugan
