GENERAL EROSION CONTROL NOTES:

1. ALL DISTURBED AREAS SHALL HAVE EROSION CONTROL PROVIDED IN ACCORDANCE WITH THE MANUAL FOR EROSION AND SEDIMENT CONTROL IN GEORGIA , CURRENT EDITION.
2. ALL EROSION CONTROL MEASURES SHALL COMPLY WITH THE STATE OF GEORGIA SOIL AND WATER CONSERVATION COMMISSION MANUAL FOR EROSION AND SEDIMENT CONTROL IN THE STATE OF GEORGIA , CURRENT EDITION.
3. FULL COORDINATION SHALL BE MAINTAINED BETWEEN THE CONTRACTOR, DESIGN PROFESSIONAL, AND THE REGULATORY INSPECTOR REGARDING PROJECT SEQUENCE.
4. THE NOTATION (XXX) AS SHOWN ON THE EROSION CONTROL PLAN SHEET(S) AND ON THE EROSION CONTROL DETAIL SHEET FOR THE EROSION AND SEDIMENT CONTROL BEST MANAGEMENT PRACTICES, REFERS TO THE GEORGIA UNIFORM CODING SYSTEM AS DETAILED IN THE MANUAL FOR EROSION AND SEDIMENT CONTROL IN GEORGIA , CURRENT EDITION.
5. GENERAL STATEMENT OF DESIGNED EROSION CONTROL SYSTEM:
   (a). NO SURFACE WATER FLOWS FROM DISTURBED AREA TO BE ALLOWED INTO THE STORM SEWER SYSTEM WITHOUT FIRST BEING FILTERED BY AN EFFECTIVE SEDIMENT ENTRAPMENT DEVICE.
   (b). SEDIMENT ENTRAPMENT DEVICES ARE TO BE MAINTAINED AT ALL POINTS WHERE SURFACE FLOWS FROM DISTURBED AREAS CAN LEAVE THE SITE. FLOWS ARE TO BE DIRECTED TO ENTRAPMENT DEVICES THROUGHOUT CONSTRUCTION ACTIVITIES.
6. EROSION CONTROL MEASURES ARE TO BE INSTALLED PRIOR TO ANY LAND DISTURBING ACTIVITIES ON-SITE AND MAINTAINED UNTIL PERMANENT GROUND COVER IS ESTABLISHED. EROSION CONTROL MEASURES SHALL BE INSPECTED AT THE END OF EACH WORKING DAY AND AFTER EACH STORM EVENT TO ENSURE THAT ALL MEASURES ARE FUNCTIONING PROPERLY. ANY REPAIRS SHALL BE MADE BY THE CONTRACTOR.
7. IN ADDITION TO THE NOTE ABOVE, EROSION AND SEDIMENT CONTROL MEASURES SHALL BE INSPECTED AT LEAST WEEKLY, AFTER EACH RAIN EVENT, AND REPAIRED AS NECESSARY THESE INSPECTIONS SHALL BE DOCUMENTED WITH COPIES SENT TO THE OWNER.
8. EROSION AND SEDIMENT CONTROL DEVICES MUST BE INSTALLED AND INSPECTED PRIOR TO ANY LAND DISTURBANCE ON SITE. SILT BARRIER TO BE PLACED AS SHOWN AND/OR AS DIRECTED BY THE PROJECT ENGINEER AND/OR OWNER: RICHMOND COUNTY SCHOOL SYSTEM.
9. THE ESCAPE OF SEDIMENT FROM THE SITE SHALL BE PREVENTED BY THE INSTALLATION OF EROSION AND SEDIMENT CONTROL MEASURES AND PRACTICES, PRIOR TO, OR CONCURRENT WITH, LAND DISTURBING ACTIVITIES.
10. EROSION AND SEDIMENTATION CONTROL MEASURES WILL BE MAINTAINED AT ALL TIMES. IF FULL IMPLEMENTATION OF THE APPROVED PLAN DOES NOT PROVIDE FOR EFFECTIVE EROSION CONTROL, ADDITIONAL EROSION AND SEDIMENT CONTROL MEASURES SHALL BE IMPLEMENTED TO CONTROL OR TREAT THE SEDIMENT SOURCE.
11. ANY DISTURBED AREA LEFT IDLE/EXPOSED FOR A PERIOD GREATER THAN 14-DAYS SHALL BE STABILIZED WITH MULCH OR TEMPORARY SEEDING; DISTURBED AREAS IDLE/EXPOSED 30-DAYS SHALL BE STABILIZED WITH PERMANENT VEGETATION.
12. ADDITIONAL EROSION AND SEDIMENT CONTROL MEASURES SHALL BE INSTALLED IF DETERMINED NECESSARY BY ON-SITE INSPECTION.
13. THE CONTRACTOR SHALL COMPLETELY REMOVE ALL TEMPORARY EROSION AND SEDIMENT CONTROL DEVICES (I.E. SILT FENCE, SEDIMENT TRAPS, ETC...) AND TREE PROTECTION FENCING ONCE PERMANENT VEGETATION IS ESTABLISHED.
14. THE CONTRACTOR IS RESPONSIBLE FOR MONITORING DOWNSTREAM CONDITIONS THROUGHOUT THE CONSTRUCTION PERIOD AND FOR CLEARING ANY DEBRIS AND SEDIMENT THAT IS CAUSED BY CONSTRUCTION ACTIVITIES.
15. ALL DISTURBED AREAS SHALL BEST BE STABILIZED AS REQUIRED BY THESE PLANS BY THE SITEWORK CONTRACTOR AS SOON AS CONSTRUCTION PHASES PERMIT.
16. WHEN HAND PLANTING, MULCH (HAY OR STRAW) SHOULD BE UNIFORMLY SPREAD OVER SEEDED AREA WITHIN 24-HOURS OF SEEDING.
17. DURING UNSUITABLE GROWING SEASONS, MULCH WILL BE USED AS A TEMPORARY COVER (Ds1). ON SLOPES 4:1 OR STEEPER, MULCH WILL BE ANCHORED.
18. SILT FENCE SHALL MEET THE MINIMUM REQUIREMENTS OF SECTION 171 OF THE STATE OF GEORGIA DEPARTMENT OF TRANSPORTATION, STANDARD SPECIFICATIONS, CURRENT EDITION, AND/OR GEORGIA EPD "GREEN BOOK" AS AMENDED.
19. SEDIMENT STORAGE MAINTENANCE INDICATORS MUST BE INSTALLED IN SEDIMENT STORAGE STRUCTURES, INDICATING THE 1/3 FULL VOLUME FOR RETROFITS AND TEMPORARY SEDIMENT BASINS, AND THE 1/2 FULL VOLUME FOR ALL OTHER SEDIMENT STORAGE STRUCTURES (I.E. CHECK DAMS, SILT FENCE, ETC...).
20. ALL SEDIMENT STORAGE DEVICES ARE TO BE CONSTRUCTED COMPLETELY AND FULLY OPERATIONAL PRIOR TO ANY OTHER CONSTRUCTION OR GRADING.
21. CONCENTRATED FLOW AREAS AND ALL SLOPES STEEPER THAN 2.5:1 WITH A HEIGHT OF TEN FEET OR GREATER SHALL BE STABILIZED WITH APPROPRIATE EROSION CONTROL MATTING AND BLANKETS.
22. ALL PERMANENT GRADED EARTH SLOPES, EXCAVATION OR EMBANKMENT (CUT AND FILL), SHALL BE GRADED TO A MAXIMUM FINISHED SLOPE OF TWO (2) FEET HORIZONTAL TO ONE (1) FOOT VERTICAL (MAXIMUM SLOPE 2H:1V).
23. ALL DISTURBED AREAS LEFT MULCHED AFTER 30-DAYS SHALL BE STABILIZED WITH TEMPORARY GRASSING.
24. SEDIMENT SHALL NOT BE WASHED INTO INLETS. IT SHALL BE REMOVED FROM THE SEDIMENT TRAPS AND DISPOSED OF AND STABILIZED SO THAT IT WILL NOT ENTER THE INLETS.
25. FAILURE TO INSTALL, OPERATE, OR MAINTAIN ALL EROSION CONTROL MEASURES WILL RESULT IN ALL CONSTRUCTION BEING STOPPED ON THE JOB UNTIL SUCH MEASURES ARE CORRECTED BACK TO THE APPROVED EROSION CONTROL PLANS, I.E., MANDATORY STOP WORK ORDER.
26. THE CONSTRUCTION EXIT SHALL BE MAINTAINED IN A CONDITION WHICH WILL PREVENT TRACKING OR FLOW OF MUD ONTO PUBLIC RIGHT-OF-WAY. THIS MAY REQUIRE PERIODIC TOP DRESSING WITH 1-3" STONE, AS CONDITIONS DEMAND, AND REPAIR AND/OR CLEAN-OUT OF ANY STRUCTURES USED TO TRAP SEDIMENT. ALL MATERIALS SPILLED, DROPPED, WASHED, OR TRACKED FROM A VEHICLE OR FROM THE SITE ONTO PUBLIC ROADWAY OR INTO STORM DRAINS MUST BE REMOVED IMMEDIATELY.

INITIAL PHASE (CLEARING & GRUBBING) NOTES:

1. ALL STAGING AREAS, MATERIAL STORAGE AREAS, CONCRETE WASH-OUT AREAS, SHALL BE LOCATED AT SETBACK DISTANCES FROM DESIGNATED TREE PROTECTION AREAS AND/OR STREAM BUFFERS AS REQUIRED BY LOCAL AND STATE REGULATIONS.
2. A COPY OF THE APPROVED LAND DISTURBANCE PLAN AND PERMIT SHALL BE PRESENT ON THE SITE AT ALL TIMES. POST ON DAY ONE.
3. PRIOR TO COMMENCING LAND DISTURBING ACTIVITY, THE LIMITS OF LAND DISTURBANCE SHALL BE CLEARLY AND ACCURATELY DELINEATED WITH STAKES, RIBBONS, OR OTHER APPROPRIATE MEANS. THE LOCATION AND EXTENT OF ALL AUTHORIZED LAND DISTURBANCE ACTIVITY SHALL BE DEMARCATED FOR THE DURATION OF THE CONSTRUCTION ACTIVITY. NO LAND DISTURBANCE SHALL OCCUR OUTSIDE THE APPROVED LIMITS INDICATED ON THE APPROVED PLANS.
4. PRIOR TO ANY OTHER CONSTRUCTION, A STABILIZED CONSTRUCTION EXIT (Co) SHALL BE CONSTRUCTED AT EACH POINT OF ENTRY TO OR EXIT FROM THE SITE OR ONTO ANY PUBLIC ROADWAY AS SHOWN ON THE PLANS.
   LOCATION:
   LATITUDE: 33.456364 N LONGITUDE: 82.002622 W
5. IMMEDIATELY AFTER THE ESTABLISHMENT OF CONSTRUCTION ENTRANCE/EXITS, ALL PERIMETER EROSION CONTROL AND STORMWATER MANAGEMENT DEVICES SHALL BE INSTALLED AS SHOWN ON THE INITIAL PHASE OF THE EROSION CONTROL PLAN.
6. SILT FENCE OR APPROVED EQUAL SHALL BE INSTALLED AT THE PERIMETER OF THE DISTURBED AREA OR AS SHOWN ON THE PLAN. SILT SHOULD BE REMOVED WHEN ACCUMULATION REACHES HALF THE HEIGHT OF THE BARRIER. THE PERIMETER SILT FENCE SHOULD BE INSPECTED DAILY FOR ANY FAILURES. ANY FAILURES OF SAID FENCING SHOULD BE REPAIRED IMMEDIATELY.
7. INLET SEDIMENT PROTECTION MEASURES SHALL BE INSTALLED ON ALL EXISTING STORM STRUCTURES AS SHOWN ON THE PLAN.
8. TREE PROTECTION FENCING AND STREAM BUFFER LIMITS SHOULD BE INSTALLED PRIOR TO THE START OF ANY LAND DISTURBING ACTIVITY AND MAINTAINED UNTIL FINAL LANDSCAPE IS INSTALLED. THE TREE PROTECTION FENCING SHOULD BE INSPECTED DAILY. ANY FAILURES OF SAID FENCING SHOULD BE REPAIRED IMMEDIATELY.
9. AFTER INSTALLATION OF INITIAL EROSION CONTROL MEASURES, THE SITE CONTRACTOR SHALL SCHEDULE AN INSPECTION BY THE PROJECT DESIGN PROFESSIONAL WITHIN 7 DAYS AFTER INSTALLATION. NO OTHER CONSTRUCTION ACTIVITIES SHALL OCCUR UNTIL THE PROJECT PROFESSIONAL APPROVES THE INSTALLATION OF SAID EROSION MEASURES. IF UNFORESEEN CONDITIONS EXIST IN THE FIELD THAT WARRANT ADDITIONAL EROSION CONTROL MEASURES, THE CONTRACTOR MUST CONSTRUCT ANY ADDITIONAL EROSION CONTROL DEVICES DEEMED NECESSARY BY THE SITE INSPECTION WITH CONSULTATION WITH THE DESIGN PROFESSIONAL.
10. AFTER APPROVAL OF THE INITIAL EROSION CONTROL INSTALLATION, THE CONTRACTOR MAY PROCEED WITH CLEARING AND GRUBBING ACTIVITIES. AS CLEARING PERMITS, THE CONTRACTOR SHALL CONSTRUCT TEMPORARY SEDIMENT STORAGE DEVICES AS SHOWN ON THE INITIAL PHASE PLAN TO CONTROL EROSION AND STORMWATER RUNOFF.
11. INITIAL PHASE BMPs UTILIZED IN THIS PLAN(S) ARE AS FOLLOWS:
    Co, Sd1-NS, Sd2-F

INTERMEDIATE PHASE (GRADING & TEMPORARY VEGETATION) NOTES:

1. MAINTAIN PREVIOUSLY INSTALLED BMPs.
2. SCHEDULING AND PERFORMANCE TO ENSURE THAT LAND STRIPPED OF ITS NATURAL GROUND COVER IS EXPOSED ONLY IN SMALL QUANTITIES, AND THEREFORE LIMITED DURATIONS, BEFORE PERMANENT EROSION PROTECTION IS ESTABLISHED.
3. GROUND DISTURBANCE OCCURS. THE LOCATION OF SOME OF THE EROSION CONTROL DEVICES MAY HAVE TO BE ALTERED FROM THAT SHOWN ON THE APPROVED PLANS IF DRAINAGE PATTERNS DURING CONSTRUCTION ARE DIFFERENT FROM THE FINAL PROPOSED DRAINAGE PATTERNS. IT IS THE CONTRACTOR'S RESPONSIBILITY TO ACCOMPLISH EROSION CONTROL FOR ALL DRAINAGE PATTERNS CREATED AT VARIOUS STAGES DURING CONSTRUCTION. ANY DIFFICULTY IN CONTROLLING EROSION AND SEDIMENTATION DURING ANY PHASE OF CONSTRUCTION SHALL BE REPORTED TO THE DESIGN PROFESSIONAL IMMEDIATELY.
4. THE SILT FENCE SHALL BE MAINTAINED UNTIL PERMANENT GROUND COVER IS ESTABLISHED. SILT SHALL BE REMOVED WHEN ACCUMULATION REACHES HALF OF THE HEIGHT OF THE BARRIER.
5. SILT FENCE SHALL BE PLACED AT THE TOE OF ALL DIRT STOCK PILE AREAS.
6. AFTER PRELIMINARY CLEARING AND GRADING ACTIVITIES, THE CONTRACTOR SHALL CONSTRUCT ALL SEDIMENT ENTRAPMENT DEVICES AS SHOWN ON THE PLANS. THE CONTRACTOR SHALL MAINTAIN THE DEVICES UNTIL PERMANENT GROUND COVER IS ESTABLISHED. SEDIMENT SHALL BE CLEANED OUT WHEN IT REACHES THE CLEAN-OUT ELEVATION SHOWN ON THE PLANS.
7. SEDIMENT AND EROSION CONTROL MEASURES MUST BE CHECKED WEEKLY AND AFTER EACH RAIN EVENT. EACH DEVICE IS TO BE MAINTAINED OR REPLACED IF SEDIMENT ACCUMULATION HAS REACHED ONE HALF OF THE CAPACITY OF THE DEVICE. ADDITIONAL DEVICES MUST BE INSTALLED IF NEW CHANGES HAVE DEVELOPED.
8. INTERMEDIATE PHASE BMPs UTILIZED ON THIS PLAN(S) ARE AS FOLLOWS:
   Du, Ds1, Ds2, Sd2-F

FINAL PHASE (STORMWATER MANAGEMENT & PERMANENT VEGETATION) NOTES:

1. THE CONTRACTOR SHALL MAINTAIN ALL SEDIMENT DEVICES AND EROSION CONTROL MEASURES UNTIL PERMANENT GROUND COVER IS ESTABLISHED. SEDIMENT SHALL BE CLEANED OUT OF EACH DEVICE WHEN IT REACHES THE REQUIRED CLEAN-OUT ELEVATION SHOWN ON THE PLANS.
2. AFTER CURBING AND PAVEMENT HAS BEEN INSTALLED, ALL INLET SEDIMENT TRAPS ON THE EXISTING INLETS SHALL BE REMOVED AND REPLACED WITH CURB FILTER INLET PROTECTION.
3. FINAL STABILIZATION OF PERMANENT GRASS MUST MEET 100% COVERAGE, 70% DENSITY RULE.
4. FINAL PHASE BMPs UTILIZED ON THIS PLAN(S) ARE AS FOLLOWS:
   Ds3, WATER QUALITY FEATURE

GRASSING:

1. SEPTEMBER 15 - FEBRUARY 15, A MIXTURE OF UNHULLED COMMON BERMUDA 6 LBS./ACRE AND RYE GRASS SEED 28 LBS./ACRE APPLIED SIMULTANEOUSLY.
2. OCTOBER 1 - MARCH 1, UNHULLED COMMON BERMUDA 10 LBS./ACRE.
3. APRIL 1 - JUNE 1, HULLED COMMON BERMUDA 10 LBS./ACRE.
4. FERTILIZER GRADE WILL BE A COMMERCIAL 6-12-12 INCORPORATED INTO THE SOIL AT 1500 LBS./ACRE, ALSO 1500 LBS. DOLOMITIC LIME.
5. NOT LESS THAN 30 DAYS AFTER SEEDING, APPLY AMMONIUM NITRATE (NOT LESS THAN 20% NITRATE) AT A RATE EQUAL TO 60 LBS. OF AVAILABLE NITROGEN /ACRE. APPLICATION BETWEEN JUNE THRU AUGUST.
6. ALL SEEDED AREAS WILL BE MULCHED WITH STRAW OR HAY MULCH AT A RATE OF 2.5 TONS/ACRE.
7. FOR ALL DATES NOT COVERED UNDER THE GRASSING SCHEDULE THE DISTURBED SOIL SHALL BE TEMPORARILY STABILIZED USING POLYACRYLAMIDE.

GRASSING:

1. ONSITE DRAINAGE BASIN = 12.4 ACRES (MULTIPLE BASINS)
2. OFFSITE DRAINAGE BASIN = 0.16 SQUARE MILES
3. CONTRACTOR TO ENSURE THAT EXISTING ON SITE VEGETATION OUTSIDE THE LIMITS OF CONSTRUCTION IS PRESERVED AND THAT ALL DISTURBED PORTIONS OF THE SITE ARE STABILIZED.
4. ALL EROSION CONTROL DEVICES SHALL BE PROPERLY MAINTAINED DURING ALL PHASES OF CONSTRUCTION ACTIVITIES AND ALL DISTURBED AREAS HAVE BEEN STABILIZED. ADDITIONAL CONTROL DEVICES MAY BE REQUIRED DURING CONSTRUCTION IN ORDER TO CONTROL EROSION AND/OR OFFSITE SEDIMENTATION. ALL TEMPORARY CONTROL DEVICES SHALL BE REMOVED ONCE CONSTRUCTION IS COMPLETE AND THE SITE IS STABILIZED.
5. NO WATERS OF THE STATE ARE IMPACTED ON THIS PROJECT.
6. RECEIVING STREAM IS OATES CREEK TRIBUTARY NO.1. SHEET C100 ON PLANS

THE PRIMARY PERMITTEE SHALL PROVIDE A COPY OF THE APPROVED EROSION, SEDIMENTATION & POLLUTION CONTROL PLAN AND ANY SUBSEQUENT REVISIONS TO THE PLAN TO EACH SECONDARY PERMITTEE.

NAME	ADDRESS	PLANS RECIEVED BY/DATE

STORMWATER CALCULATIONS:

1. REQUIRED STORMWATER STORAGE = 0.00 CY (AS DETERMINED BY LOCAL ORDINANCE)
2. REQUIRED SEDIMENT STORAGE = 360 CY (67 CY/ACRE x 5.37 ACRES DISTURBED AREA)
3. TOTAL REQUIRED STORAGE = 0.00 CY + 360 CY = 360 CY
4. AVAILABLE STORAGE = 372 CY
5. IS THE AVAILABLE STORAGE (X.XX CY) GREATER THAN STORAGE REQUIRED (X.XX CY)?
   ☒ YES ☐ NO
6. IF "NO", THE SEDIMENT STORAGE CAPACITY OF THE POND MUST ME INCREASED. CHOOSE THE METHOD TO BE USED:
   ☐ RAISE THE INVERT OF THE OUTLET STRUCTURE:______INCHES.
   ☐ UNDERCUT THE POND:______FEET.
   ☐ OTHER:______.
7. CLEAN-OUT ELEVATION = WEIR B1&2 = 252.4 FEET, WEIR A5 = 152.9 FEET. (ELEVATION CORRESPONDING TO 22 CY/ACRE x 5.37 ACRES DISTURBED AREA)
8. IS THE LENGTH-WIDTH RATIO 2:1 OR GREATER?
   ☒ YES ☐ NO
9. IF "NO", THE LENGTH OF FLOW MUST BE INCREASED
   ☐ BAFFLES (TYPE OF BAFFLE:______.
   ☐ OTHER:______.

NOTE THE CMP DIAMETER AND HEIGHT IF A HALF-ROUND CMP RETROFIT IS TO BE USED:
DIAMETER = 24 INCHES HEIGHT = 4 FEET

SEDIMENT STORAGE:

REQUIRED: 5.37 ACRES x 67 CY/ACRE = 360 CY
PROVIDED BY Sd2: RECTANGULAR EXCAVATED INLET SEDIMENT TRAP
*SEE H&H REPORT FOR SEDIMENT STORAGE AND SD2-E SIZING CALCULATIONS
TOTAL AVAILABLE STORAGE = 372 CY

APPROXIMATE START DATE: JANUARY 2019
APPROXIMATE FINISH DATE: FEBRUARY 2020

MONTHS OF CONSTRUCTIONS ACTIVITIES



NOTES:
1. ALL DISTURBED AREAS NOT INTENDED FOR PAVING SHALL BE STABILIZED USING TEMPORARY MEASURES Ds2 AND PERMANENT MEASURES Ds3.

SITE SOIL TYPE	
SOIL MAP SYMBOL	SOIL NAME
DhA	DOGUE-URBAN LAND COMPLEX, 0 TO 3 PERCENT SLOPES
Rh	RAINS-URBAN LAND COMPLEX
Ud	URBAN LAND

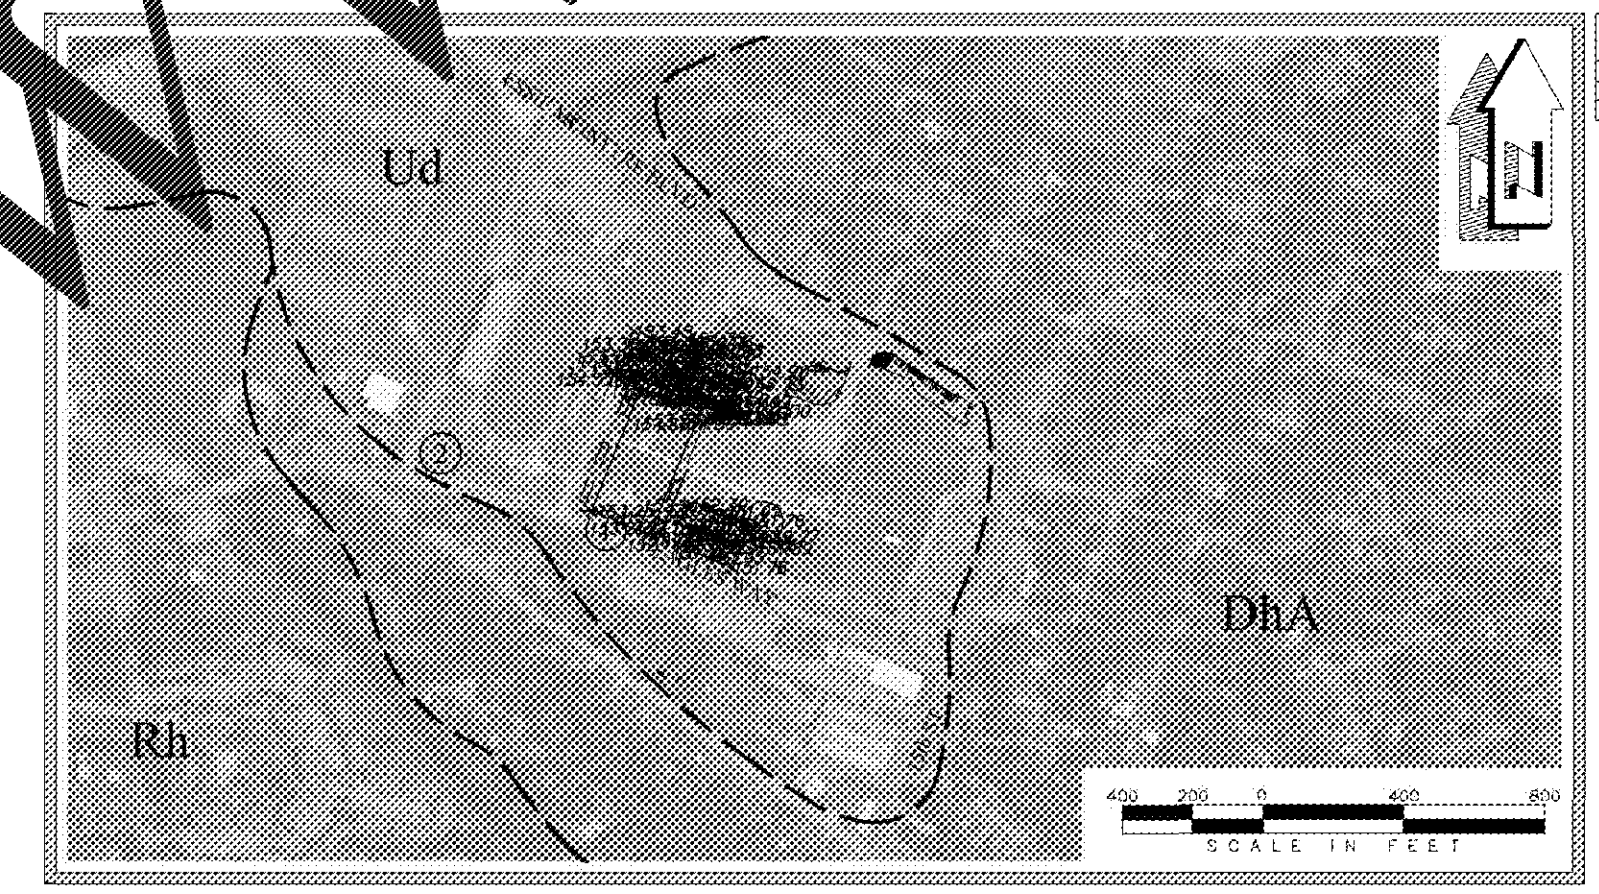

MONITORING PLAN & SOILS MAP
1"=100'

NTU VALUE: 50
SITE SIZE: 6.05 ACRES
DRAINAGE AREA: 0.16 SQUARE MILES

MONITORING POINTS
MONITORING POINT LOCATIONS ARE SHOWN ABOVE:

(1) WEIR INLET STRUCTURE IN EAGLES WAY
(2) GRATE TRAP BY FIELD HOUSE
(3) STORM MANHOLE BY PARENT PICKUP AREA

NOTE:
THESE ARE STANDARD NOTES PROVIDED BY THE LOCAL ISSUING AUTHORITY AND MODIFIED BY THE DESIGN PROFESSIONAL.

GEORGIA811
www.Georgia811.com

24-HOUR LOCAL ES&PC CONTACT:
NAME: BENTON STARKS
PHONE: (706) 737-7189
EMAIL: BENTON@BOE.RICHMOND.K12.GA.US

CRANSTON
ENGINEERING
ENGINEERS - PLANNERS - SURVEYORS
452 Ellis Street, Augusta, Georgia 30901
Post Office Box 2086, Augusta, Georgia 30903
Telephone 706-722-1588
mail@cranstonEngineering.com

GEORGIA REGISTERED No. PE35685 PROFESSIONAL ENGINEER MITCHELL B. MURCHISON
11/20/18

GSWCC LEVEL II
CERTIFICATION NO. 46296
EXPIRES: 10/12/19

Murphey Middle School
PE Building

Erosion Control Notes

DRAWN BY:	MAB/RDS
CHECKED BY:	TMP
APPROVED BY:	MBM
DATE:	NOVEMBER 2, 2018
SCALE:	AS SHOWN
JOB No.	2018-0178
DRAWING No.	C602

dickinson
ARCHITECTS
Architecture|Interior Design|Planning
771 Broad Street Suite 200
Augusta, Georgia 30901
706-722-7488
mail@dickinsonarchitects.com
www.dickinsonarchitects.com

Member of the American Institute of Architects

THIS DRAWING IS THE PROPERTY OF DICKINSON ARCHITECTS, P.C., AND IS NOT TO BE REPRODUCED OR COPIED IN WHOLE OR IN PART OR USED FOR FURNISHING INFORMATION TO OTHERS, OR FOR ANY OTHER PURPOSE DETRIMENTAL TO THE INTEREST OF DICKINSON ARCHITECTS, P.C., AND IS TO BE RETURNED UPON REQUEST.
©DICKINSON ARCHITECTS, P.C.

PROJECT TITLE:
MURPHEY MIDDLE SCHOOL PE BUILDING PROJECT #
B-17-005-3756.1

REVISIONS			
REV #	DATE	APRVD BY	REVISION
	11/02/18	MBM	STATE FINAL
	11/20/18	MBM	ISSUE FOR BID

DA PROJECT NUMBER & NAME:
1707.1

DRAWING TITLE:
EROSION CONTROL NOTES

DRAWING NO:
C602

2018-0178

G:\AA-ACTIVE JOB FILES\2018\2018-0178 - MURPHEY MIDDLE SCHOOL PE BUILDING AND PARKING IMPROVEMENTS\AC-DRAWINGS\CIVIL\20180178_COVR.DWG 11/21/2018 9:57 AM

Order Plans @ www.LDILine.com
