STORMWATER POLLUTION PREVENTION NOTES

THESE PLANS HAVE BEEN PREPARED TO ASSIST THE CONTRACTOR IN OBTAINING COVERAGE UNDER THE FDEP GENERIC PERMIT FOR STORMWATER DISCHARGE FROM LARGE AND SMALL CONSTRUCTION ACTIVITIES. IT IS THE CONTRACTOR'S RESPONSIBILITY TO REVIEW THE PERMIT REQUIREMENTS AND MODIFY THESE PLANS AS NEEDED TO BE IN COMPLIANCE WITH THE PERMIT REQUIREMENTS.

SITE DESCRIPTION.

A. SITE LOCATION
THE SITE IS LOCATED AT ATLANTIC BLVD. & KERNAN , IN THE CITY OF JACKSONVILLE, DUVAL COUNTY, FLORIDA
SECTION 21, TOWNSHIP 02 SOUTH, RANGE 28 EAST
LATITUDE: 30° 19'16.92"N LONGITUDE: 81 °29'40.42"W

B. SITE CONDITIONS & ACTIVITIES NARRATIVE
THE EXISTING CONDITION OF THE SITE IS "VACANT LAND". DURING CONSTRUCTION THE SITE WILL BE CLEARED AND GRUBBED. THIS PROJECT WILL HAVE NO MAJOR EFFECT ON ANY THE ABUTTING PROPERTIES.

WETLANDS/BUFFERS

NO WETLANDS OR BUFFERS ARE ASSOCIATED WITH THIS PROJECT.

SWPPP INTENT

THE INTENT OF THIS SWPPP IS TO COMPLY WITH THE INTENT OF THE GENERIC PERMIT AND TO PREVENT THE RELEASE OF SOILS, TRASH, CHEMICALS, TOXINS AND OTHER POLLUTANTS, BY WATER , AIR, VEHICLE TRANSPORT OR OTHER MEANS THAT CAN IMPACT STORM WATER QUALITY. THE CONTRACTOR SHALL OBTAIN A COPY OF THE GENERIC PERMIT AND RETAIN ON-SITE FOR FUTURE REFERENCE. THE CONTRACTOR SHALL READ AND UNDERSTAND THE PERMIT, AND ENSURE THAT THE BMP'S ARE INSTALLED AND THE EXECUTION OF THE WORK IS PERFORMED TO MEET THE INTENT OF THE GENERIC PERMIT AND THE SWPPP.

POTENTIAL SOURCES OF POLLUTION

THE POTENTIAL SOURCES OF POLLUTION THAT MAY REASONABLY BE EXPECTED TO AFFECT THE QUALITY OF STORM WATER DISCHARGE ASSOCIATED WITH CONSTRUCTION ACTIVITY INCLUDE: SEDIMENT, PESTICIDES, FERTILIZER, PLASTER, CLEANING SOLVENTS, ASPHALT, CONCRETE, GLUE, ADHESIVES, PAINTS, CURING COMPOUNDS, WOOD PRESERVATIVES, HYDRAULIC OIL FLUIDS, GASOLINE, DIESEL FUEL AND KEROSENE.

SEQUENCE OF CONSTRUCTION.

THE SEQUENCE OF CONSTRUCTION HAS BEEN DEVELOPED AS A GUIDE FOR THE CONTRACTOR. THE CONTRACTOR SHALL SEQUENCE THE CONSTRUCTION AS NEEDED BASED ON BEST MEANS AND METHODS IN ORDER TO BE IN COMPLIANCE WITH STATE AND LOCAL REQUIREMENTS. THE INSTALLATION OR REMOVAL OF BMPS, EARTH DISTURBANCE, GRADING, TEMPORARY STABILIZATION AND PERMANENT STABILIZATION SHALL BE IMMEDIATELY NOTED IN THE SWPPP IMPLEMENTATION LOG. ALL TEMPORARY BMPS SHALL BE REPAIRED AND MAINTAINED UNTIL STABILIZATION HAS OCCURRED AND THERE IS NO RISK OF DISCHARGE. TEMPORARILY SEED, IMMEDIATELY AND THROUGHOUT CONSTRUCTION, DENUDED AREAS THAT WILL BE INACTIVE FOR 7 DAYS OR MORE. PERMANENTLY STABILIZE AREAS TO BE VEGETATED AS THEY ARE BROUGHT TO FINAL GRADE.

1. POST A COPY OF THE NOI OR LETTER FROM FDEP CONFIRMING COVERAGE UNDER THE GENERIC PERMIT, AND THE NAME AND PHONE NUMBER OF THE CONTRACTOR'S REPRESENTATIVE RESPONSIBLE FOR EROSION AND SEDIMENTATION CONTROL INSTALLATION AND MAINTENANCE ON A 24 HOUR BASIS.
2. INSTALL PERIMETER CONTROLS IMMEDIATELY DOWNSTREAM OF THE PLANNED LOCATION OF THE CONSTRUCTION EXIT.
3. INSTALL STABILIZED CONSTRUCTION EXIT.
4. INSTALL PERIMITER CONTROLS. THE CONTRACTOR SHALL INSTALL THE REMAINING BMPS AS SHOWN AND AS REQUIRED TO MEET PERMIT REQUIREMENTS. SOME BMP INSTALLATIONS MAY NOT BE POSSIBLE AT THE BEGINNING OF THE PROJECT BUT MUST BE INSTALLED AS SOON AS POSSIBLE TO ENSURE COMPLIANCE.
5. INSTALL TEMPORARY STAGING AND STORAGE AREAS.
6. CONSTRUCT AND STABILIZE THE SEDIMENT BASINS AND SEDIMENT TRAPS WITH APPROPRIATE OUTFALL STRUCTURES, IF REQUIRED.
7. CONSTRUCT AND STABILIZE HYDRAULIC CONTROLS (DITCHES, SWALES, DIKES, CHECK DAMS, ETC.), IF REQUIRED.
8. BEGIN DEMOLITION, CLEARING AND GRUBBING OPERATIONS AS APPLICABLE.
9. BEGIN CONSTRUCTION OF SITE IMPROVEMENTS.
10. PAVE SITE AND STABILIZE PER PLAN.
11. REMOVE ALL TEMPORARY EROSION AND SEDIMENT CONTROL DEVICES AFTER SITE HAS ACHIEVED FINAL STABILIZATION.
12. SUBMIT NOTICE OF TERMINATION (NOT) ONCE ALL CONSTRUCTION IS COMPLETE AND ALL AREAS ARE STABILIZED PER PLAN.

GENERAL NOTES

A. IT IS THE CONTRACTOR'S RESPONSIBILITY TO FILE "NOTICE OF INTENT TO USE GENERIC PERMIT FOR STORMWATER DISCHARGE FROM CONSTRUCTION ACTIVITIES" (DEP FORM 62-621.300(4)(B) OR LATEST VERSION) TO FDEP TO THE FOLLOWING ADDRESS OR THROUGH THE FDEP ON-LINE SYSTEM AT LEAST TWO (2) DAYS BEFORE COMMENCEMENT OF CONSTRUCTION:

NPDES STORMWATER NOTICES CENTER, MS #2510 FLORIDA DEPARTMENT OF ENVIRONMENTAL PROTECTION, 2600 BLAIR STONE ROAD, TALLAHASSEE, FLORIDA 32399-2400

THE CONTRACTOR SHALL SUBMIT A NOTICE OF TERMINATION (NOT) WITHIN 14 CALENDAR DAYS AFTER THE SITE HAS ACHIEVED FINAL STABILIZATION (I.E. ALL DISTURBED SOILS AT THE SITE HAVE BEEN FINAL STABILIZED), TEMPORARY BMPS HAVE BEEN REMOVED, AND STORMWATER DISCHARGES ASSOCIATED WITH CONSTRUCTION ACTIVITY FROM THE SITE AUTHORIZED BY THE PERMIT HAVE BEEN ELIMINATED.

AN ENVIRONMENTAL RESOURCE PERMIT IS REQUIRED FOR THE PROJECT. CONTRACTOR SHALL PROVIDE THE PERMIT INFORMATION ON THE NOI APPLICATION.

MS4 OPERATOR NAME (IF ANY): XXXXX

THE CONTRACTOR SHALL PROVIDE A COPY OF THE NOI AND SUBSEQUENT NOT OR THE ACKNOWLEDGEMENT LETTERS FOR THE NOI OR NOT TO THE MS4 WITHIN 7 DAYS OF RECEIPT. THE CONTRACTOR SHALL ALSO COORDINATE WITH THE MS4 TO ENSURE THAT ALL SPECIFIC REQUIREMENTS ARE MET.

B. WHERE PRACTICAL, STORMWATER SHALL BE CONVEYED BY SWALES. SWALES SHALL BE CONSTRUCTED AS SHOWN ON PLANS.

C. EROSION CONTROL MEASURES SHALL BE EMPLOYED TO MINIMIZE TURBIDITY OF SURFACE WATERS LOCATED DOWNSTREAM OF ANY CONSTRUCTION ACTIVITY. WHILE THE VARIOUS MEASURES REQUIRED WILL BE SITE SPECIFIC, THEY SHALL BE EMPLOYED AS NEEDED IN ACCORDANCE WITH THE FOLLOWING:

I. IN GENERAL, EROSION SHALL BE CONTROLLED AT THE FURTHEST PRACTICAL UPSTREAM LOCATION.
II. NEW AND EXISTING STORMWATER INLETS AND OUTFALL STRUCTURES SHALL BE PROTECTED DURING CONSTRUCTION. PROTECTION MEASURES SHALL BE EMPLOYED IMMEDIATELY AS REQUIRED DURING THE VARIOUS STAGES OF CONSTRUCTION.
III. PERIMETER EROSION CONTROL DEVICES SHALL REMAIN IN PLACE UNTIL FINAL SITE STABILIZATION HAS BEEN ESTABLISHED

D. CLEARING AND GRUBBING OPERATIONS SHALL BE CONTROLLED SO AS TO MINIMIZE UNPROTECTED ERODIBLE AREAS EXPOSED TO WEATHER. GENERAL EROSION CONTROL BMP'S SHALL BE EMPLOYED TO MINIMIZE SOIL EROSION AND OFF-SITE SEDIMENTATION. WHILE THE VARIOUS TECHNIQUES REQUIRED WILL BE SITE AND PLAN SPECIFIC, THEY SHOULD BE EMPLOYED PRIOR TO ANY CONSTRUCTION ACTIVITY.

E. THE CONTRACTOR SHALL FURNISH, INSTALL PER THE SEQUENCE OF CONSTRUCTION, MAINTAIN AND SUBSEQUENTLY REMOVE, ALL NECESSARY TEMPORARY BMPS. THE CONTRACTOR WILL FURNISH AND INSTALL ALL NECESSARY PERMANENT BMPS.

F. THE CONTRACTOR SHALL ADJUST, ADD OR MODFY BMPS AS NECESSARY TO COMPLY WITH THE INTENT OF THE GENERIC NPDES PERMIT AND THE SWPPP FOR NO ADDITIONAL COMPENSATION. THE CONTRACTOR SHALL CONSULT WITH THE ENGINEER PRIOR TO ADJUSTING, ADDING OR MODIFYING BMPS THAT AFFECT THE HYDRAULICS OF THE SITE OR BEFORE ADDING BMPS NOT DETAILED IN THE SWPPP.

G. THE CONTRACTOR IS ADVISED THAT THE CONTRACT DRAWINGS ONLY INDICATE EROSION, SEDIMENT, AND TURBIDITY CONTROLS AT LOCATIONS DETERMINED IN THE DESIGN PROCESS. HOWEVER, THE CONTRACTOR IS REQUIRED TO PROVIDE ANY ADDITIONAL CONTROLS NECESSARY TO PREVENT THE POSSIBILITY OF SILTING ANY ADJACENT LOWLAND PARCEL OR RECEIVING WATER.

H. EROSION AND SEDIMENT CONTROL MEASURES ARE TO BE PLACED PRIOR TO, OR AS THE FIRST STEP IN CONSTRUCTION. THE CONTRACTOR IS RESPONSIBLE FOR COMPLYING WITH ALL EROSION CONTROL MEASURES SHOWN ON THE PLANS. THE EROSION CONTROL SYSTEM DESCRIBED WITHIN THE CONSTRUCTION DOCUMENTS SHOULD BE CONSIDERED TO REPRESENT THE MINIMUM ACCEPTABLE STANDARDS FOR THIS PROJECT. ADDITIONAL EROSION CONTROL MEASURES MAY BE REQUIRED DEPENDENT UPON THE STAGE OF CONSTRUCTION, THE SEVERITY OF THE RAINFALL EVENT AND/OR AS DEEMED NECESSARY AS A RESULT OF ON-SITE INSPECTIONS BY THE OWNER, THEIR REPRESENTATIVES, OR THE APPLICABLE JURISDICTIONAL AUTHORITIES. THESE ADDITIONAL MEASURES (IF NEEDED) SHALL BE INSTALLED AT NO ADDITIONAL COST TO THE OWNER. IT SHOULD BE NOTED THAT THE MEASURES IDENTIFIED ON THIS PLAN ARE ONLY SUGGESTED BEST MANAGEMENT PRACTICES (BMPS). THE CONTRACTOR SHALL PROVIDE POLLUTION PREVENTION AND EROSION CONTROL MEASURES AS SPECIFIED IN FDOT INDEXES #100 THROUGH #102 AND AS NECESSARY FOR EACH SPECIFIC APPLICATION. IT IS THE CONTRACTOR'S ULTIMATE RESPONSIBILITY TO ASSURE THAT THE STORMWATER DISCHARGE FROM THE SITE DOES NOT EXCEED THE TOLERANCES ESTABLISHED BY ANY OF THE APPLICABLE JURISDICTIONAL AUTHORITIES.

I. THE CONTRACTOR SHALL KEEP THE SWPPP CURRENT AT ALL TIMES. THE CONTRACTOR SHALL SIGN AND DATE ANY CHANGES TO THE SWPPP AND KEEP THEM AS ATTACHMENTS TO THE ORIGINAL PLAN. WHENEVER ANY OF THE FOLLOWING EVENTS OCCUR, THE CONTRACTOR SHALL UPDATE THE SWPPP WITHIN 7 DAYS.
I. THERE IS A CHANGE IN DESIGN, CONSTRUCTION OPERATION OR MAINTENANCE THAT HAS A SIGNIFICANT EFFECT ON THE DISCHARGE FROM THE PROJECT
II. THERE IS A NEW DISCHARGE POINT OUR OUTFALL
III. THERE IS A CHANGE IN THE LOCATION OF A DISCHARGE POINT OF OUTFALL
IV. AN INSPECTION REVEALS THAT BMPS ARE INEFFECTIVE AT ELIMINATING OR MINIMIZING POLLUTANTS IN THE STORMWATER DISCHARGED FROM THE SITE.
V. THERE IS A NEW SUBCONTRACTOR IMPLEMENTING ANY PORTION OF THE SWPPP
VI A RELEASE CONTAINING A HAZARDOUS SUBSTANCE IN AN AMOUNT EQUAL TO OR GREATER THAN A REPORTABLE QUANTITY OCCURS DURING A 24-HOUR PERIOD

J. THE CONTRACTOR SHALL ENSURE THAT THE CONTRACTOR AND ALL SUBCONTRACTORS RESPONSIBLE FOR IMPLEMENTING SWPPP CONTROL MEASURES FILL OUT THE CONTRACTOR / SUBCONTRACTOR CERTIFICATION TABLE INCLUDED IN THIS SWPPP.

K. THE CONTRACTOR SHALL COMPLETE THE CONSTRUCTION SEQUENCE TABLE INCLUDING IN THIS SWPPP PRIOR TO PROCEEDING WITH THE INSTALLATION OF BMPS AND PRIOR TO GROUND DISTURBING ACTIVITIES. THE CONTRACTOR SHALL COMPLETE THE TABLE WITH ANTICIPATED DATES IN WHICH THE BMP WILL BE UTILIZED OR THE ACTIVITY WILL OCCUR.

TURBIDITY

A. TURBIDITY REDUCTION TO NO MORE THAN 29 NTUs ABOVE BACKGROUND LEVEL PRIOR TO DISCHARGE OFF SITE.

B. CONTRACTOR TO FILE FOR A FDEP NOTICE OF INTENT (NOI) WITHIN 14 DAYS OF CONSTRUCTION COMPLETION.

STABILIZATION

A. STABILIZATION MEASURES SHALL BE INITIATED IMMEDIATELY IN PORTIONS OF THE SITE WHERE CONSTRUCTION ACTIVITIES HAVE TEMPORARILY OR PERMANENTLY CEASED AND WILL REMAIN UNDISTURBED FOR 7 DAYS OR MORE. STABILIZE BY COVERING WITH ADEQUATE AMOUNTS OF MULCH OVER SEED AND PERIODICALLY WATER TO PROMOTE AND MAINTAIN GROWTH OF THE TEMPORARY GROUNDCOVER, OR BY THE USE OF AN APPROPRIATE ALTERNATIVE BMP.

B. PERMANENT SOIL EROSION CONTROL MEASURES FOR ALL SLOPES, CHANNELS, DITCHES OR ANY DISTURBED LAND AREAS SHALL BE COMPLETED IMMEDIATELY AFTER FINAL GRADING. WHEN IT IS NOT POSSIBLE TO PERMANENTLY PROTECT A DISTURBED AREA IMMEDIATELY AFTER GRADING OPERATIONS, TEMPORARY EROSION CONTROL MEASURES SHALL BE INSTALLED. ALL TEMPORARY PROTECTION SHALL BE MAINTAINED UNTIL PERMANENT MEASURES ARE IN PLACE AND ESTABLISHED.

C. ALL GRASS SLOPES CONSTRUCTED STEEPER THAN 4H:1V SHALL BE SODDED IMMEDIATELY AFTER FINAL GRADE IS ESTABLISHED.

DUST CONTROL

A. BARE EARTH AREAS SHALL BE WATERED DURING CONSTRUCTION AS NECESSARY TO MINIMIZE THE TRANSPORT OF FUGITIVE DUST. IN NO CASE SHALL FUGITIVE DUST BE ALLOWED TO LEAVE THE SITE UNDER CONSTRUCTION.

B. AS REQUIRED AFTER COMPLETION OF CONSTRUCTION, BARE EARTH AREAS SHALL BE VEGETATED.

AT ANY TIME BOTH DURING AND AFTER SITE CONSTRUCTION THAT WATERING AND/OR VEGETATION ARE NOT EFFECTIVE IN CONTROLLING WIND EROSION AND/OR TRANSPORT OF FUGITIVE DUST, OTHER METHODS AS ARE NECESSARY FOR SUCH CONTROL SHALL BE EMPLOYED. THESE METHODS MAY INCLUDE ERECTION OF DUST CONTROL FENCES.

WASTE MANAGEMENT

A. THE CONTRACTOR SHALL ENSURE THAT ALL WASTE AND DEBRIS ARE MANAGED DAILY SUCH THAT THEY WILL NOT IMPACT STORMWATER OR LEAVE THE PERMITTED AREA, AND DISPOSED OF PROPERLY IN ACCORDANCE WITH APPLICABLE STATE, LOCAL AND FEDERAL REGULATIONS.

B. THE CONTRACTOR SHALL ENSURE THAT ALL CHEMICALS, OILS, FUELS, HAZARDOUS WASTE, UNIVERSAL WASTE AND TOXIC SUBSTANCES ARE PROPERLY MANAGED AND DISPOSED OF IN ACCORDANCE WITH APPLICABLE STATE, LOCAL AND FEDERAL REGULATIONS. THE CONTRACTOR SHALL ENSURE THAT WASTE IS NOT DISCHARGED FROM THE SITE, AND DOES NOT IMPACT STORMWATER OR GROUNDWATER.

C. THE CONTRACTOR SHALL PROVIDE APPROPRIATE AND ADEQUATE WASHOUT FACILITIES TO ENSURE THAT CHEMICALS AND WASTE IS NOT DISCHARGED FROM THE SITE, AND DO NOT IMPACT STORMWATER OR GROUNDWATER. (E.G. CONCRETE/MASONRY WASHOUT, PAINT WASHOUT, EIFS, ETC.) THE CONTRACTOR SHALL CLEAN UP SPILLS PROMPTLY AND ENSURE THAT WASHOUT AREAS ARE PROPERLY MAINTAINED TO PROVIDE ADEQUATE VOLUME TO PREVENT OVERFLOW.

D. THE CONTRACTOR SHALL PROVIDE ADEQUATE SANITARY FACILITIES FOR SITE PERSONNEL, MAINTAIN THROUGHOUT CONSTRUCTION, AND PROVIDE FOR PROPER DISPOSAL IN ACCORDANCE WITH APPLICABLE STATE, LOCAL AND FEDERAL REGULATIONS. SANITARY FACILITIES SHALL BE PROPERLY SECURED TO PREVENT TIPPING.

E. A SPILL CONTROL AND CONTAINMENT KIT (CONTAINING FOR EXAMPLE, ABSORBENT MATERIAL SUCH AS KITTY LITTER OR SAWDUST, ACID, BASE, NEUTRALIZING AGENT, BROOMS, DUST PANS, MOPS, RAGS, GLOVES, GOGGLES, PLASTIC AND METAL TRASH CONTAINERS, ETC.) SHALL BE PROVIDED AT THE CONSTRUCTION SITE AND IT'S LOCATION(S) SHALL BE IDENTIFIED WITH LEGIBLE SIGNAGE AND SHOWN ON THE SITE MAPS.
A. THE SPILL CONTROL AND CONTAINMENT KIT SHALL BE OF SUFFICIENT QUANTITIES AND APPROPRIATE CONTENT TO CONTAIN A SPILL FROM THE LARGEST ANTICIPATED PIECE OF EQUIPMENT AND FROM THE LARGEST ANTICIPATED QUANTITIES OF PRODUCTS STORED ON THE SITE AT ANY GIVEN TIME.

F. WHEN A SPILL OF REPORTABLE QUANTITIES IS DISCOVERED ON THE SITE, THE CONTRACTOR SHALL CLEAN UP ALL SPILLED MATERIALS AND DISPOSE OF IN ACCORDANCE WITH APPLICABLE LAWS AND REGULATIONS. THE CONTRACTOR SHALL NOTIFY THE APPROPRIATE AUTHORITIES IN ACCORDANCE WITH APPLICABLE LAWS AND REGULATIONS, THE OWNER AND PROJECT ENGINEER. THE CONTRACTOR SHALL RETAIN CLEANUP INFORMATION AS WELL AS DISPOSAL MANIFESTS WITH THEIR SWPPP.

MATERIALS MANAGEMENT, AND EQUIPMENT STAGING AND MAINTENANCE

A. EXCAVATED MATERIAL SHALL NOT BE DEPOSITED IN LOCATIONS WHERE IT COULD BE WASHED AWAY BY HIGH WATER OR STORM WATER RUNOFF. STOCKPILED MATERIAL SHALL BE COVERED OR ENCIRCLED WITH SEDIMENT CONTAINMENT DEVICES.

B. HEAVY CONSTRUCTION EQUIPMENT PARKING AND MAINTENANCE AREAS SHALL BE DESIGNED TO PREVENT OIL, GREASE, AND LUBRICANTS FROM ENTERING SITE DRAINAGE FEATURES INCLUDING STORMWATER COLLECTION AND TREATMENT SYSTEMS. CONTRACTORS SHALL PROVIDE BROAD DIKES OR SILT SCREENS AROUND, AND SEDIMENT SUMPS WITHIN, SUCH AREAS AS REQUIRED TO CONTAIN SPILLS OR OIL, GREASE, LUBRICANTS, OR OTHER CONTAMINANTS. CONTRACTOR SHALL HAVE AVAILABLE, AND SHALL USE, ABSORBENT FILTER PADS TO CLEAN UP SPILLS IMMEDIATELY AFTER ANY OCCURRENCE.

C. THE CONTRACTOR SHALL ENSURE THAT ALL TOXIC / HAZARDOUS SUBSTANCES AND CHEMICALS ARE PROPERLY STORED, OUT OF THE WEATHER, AND USED IN ACCORDANCE WITH MANUFACTURER'S RECOMMENDATIONS. THE CONTRACTOR SHALL ENSURE THAT THESE PRODUCTS ARE STORED AND USED IN SUCH A MANNER THAT WILL NOT NEGATIVELY IMPACT STORMWATER, GROUNDWATER OR PROTECTED SPECIES.

D. THE CONTRACTOR SHALL ENSURE THAT ALL MATERIALS, EQUIPMENT, DEBRIS, WASTE, TRAILERS, AND OTHER SUPPORT RELATED ITEMS ARE CONTAINED WITHIN THE PERMITTED LIMITS OF DISTURBANCE. THE CONTRACTOR SHALL ENSURE THAT THE STORAGE AND USE OF SUCH ITEMS DOES NOT NEGATIVELY IMPACT STORMWATER OR GROUNDWATER.

OFFSITE VEHICLE TRACKING

A. THE CONTRACTOR SHALL ENSURE THAT THE CONSTRUCTION EXIT IS USED BY ALL VEHICLES AND EQUIPMENT ENTERING OR LEAVING THE JOBSITE. THE CONTRACTOR SHALL MONITOR AND MAINTAIN THE CONSTRUCTION EXIT TO ENSURE THAT NO SOILS ARE TRACKED OFFSITE BY TIRES OR TRACKS, AND THAT NO SOILS ARE SPILLED BY TRUCKS OR EQUIPMENT LEAVING THE SITE. ALL TRACKED OR SPILLED SOILS SHALL BE SHOVELED OR SWEPT FROM THE ROADWAY AND RETURNED TO THE SITE. WATER SHALL NOT BE USED TO CLEAN THE SOILS FROM THE ROADWAY UNLESS THE WATER AND SOILS ARE RECOVERED BY THE USE OF A VACUUM TRUCK OR SIMILAR DEVICE.

FERTILIZERS, HERBICIDES AND PESTICIDES

A. THE CONTRACTOR SHALL ENSURE THAT ALL FERTILIZERS, HERBICIDES, PESTICIDES AND SIMILAR PRODUCTS ARE PROPERLY STORED, OUT OF THE WEATHER, AND APPLIED IN ACCORDANCE WITH MANUFACTURER'S RECOMMENDATIONS. THE CONTRACTOR SHALL ENSURE THAT THESE PRODUCTS ARE USED IN SUCH A MANNER THAT WILL NOT NEGATIVELY IMPACT STORMWATER, GROUNDWATER OR PROTECTED SPECIES.

B. NUTRIENTS SHALL BE APPLIED ONLY AT RATES NECESSARY TO ESTABLISH AND MAINTAIN VEGETATION.

INSPECTIONS AND MAINTENANCE

A. THE CONTRACTOR SHALL INSPECT BMPS (I.E. DISCHARGE LOCATIONS, CONSTRUCTION EXIT, PERIMETER CONTROLS, INLET PROTECTION, STABILIZATION, EROSION CONTROL, DOCUMENTATION, WASTE DISPOSAL AREAS, MATERIAL STORAGE AREAS, ETC.) TO ENSURE THAT BMPS ARE NOT CAUSING OR CONTRIBUTION TO VIOLATIONS OF WATER QUALITY STANDARDS, RESULTING IN OFFSITE SEDIMENTATION, ENSURE THAT BMPS ARE INSTALLED, MAINTAINED AND OPERATING CORRECTLY AND EFFECTIVELY, ENSURE THAT BMPS ASSOCIATED WITH STORAGE AND WASTE DISPOSAL AREAS ARE BEING USED AND MAINTAINED PROPERLY, ENSURE THAT THE CONSTRUCTION EXIT IS FUNCTION PROPERLY TO PREVENT OFFSITE TRACKING OF SEDIMENT; ENSURE THAT EROSION PREVENTION MEASURES ARE MAINTAINED, PREVENT VISIBLE EROSION OF DISTURBED AREAS AND SEDIMENTATION AT THE DISCHARGE POINTS; AND DETERMINE IF CONSTRUCTION ACTIVITIES HAVE ALTERED THE EFFECTIVENESS OF BMPS. INSPECTIONS MUST BE CONDUCTED AT LEAST ONCE EVERY SEVEN (7) CALENDAR DAYS, AND WITHIN 24 HOURS AFTER A RAINSTORM OF 0.50 INCHES OR GREATER EVEN IF IT RAINS ON THE WEEKEND OR A HOLIDAY.

B. THE CONTRACTOR SHALL REPORT ALL INSPECTION FINDINGS AND CORRECTIVE ACTIONS TAKEN AS A RESULT OF THE INSPECTION USING THE STORMWATER POLLUTION PREVENTION PLAN INSPECTION REPORT FORM PROVIDED BY FDEP OR AN EQUIVALENT FORM. INSPECTION REPORTS SHALL BE SIGNED BY THE INSPECTOR WITH A RESPONSIBLE AUTHORITY AS DEFINED BY THE PERMIT. INSPECTION REPORTS SHALL BE MAINTAINED WITH THE SWPPP. THE INSPECTOR MUST BE A QUALIFIED EROSION AND SEDIMENT CONTROL INSPECTOR AS DEFINED BY THE FLORIDA DEPARTMENT OF ENVIRONMENTAL PROTECTION.

C. ANY MAINTENANCE, REPAIR AND NECESSARY REVISIONS TO ITEMS SHOWN ARE ADDRESSED IN A TIMELY MANNER, BUT IN NO CASE LATER THAN 7 CALENDAR DAYS FOLLOWING THE INSPECTION AND IDENTIFICATION OF THE ISSUE. UNLESS OTHERWISE SPECIFIED, ACCUMULATED SEDIMENTS SHOULD BE REMOVED BEFORE THEY REACH ONE-HALF OF THE CAPACITY OF THE CONTROL DEVICE.

ALLOWABLE NON-STORMWATER DISCHARGES

THE GENERIC PERMIT FOR STORMWATER DISCHARGES ASSOCIATED WITH CONSTRUCTION ACTIVITIES PROHIBIT MOST NON-STORMWATER DISCHARGES DURING THE CONSTRUCTION PHASE. CERTAIN DISCHARGES ARE ALLOWED BY THE PERMIT, PROVIDED APPROPRIATE BMPS ARE UTILIZED AND THE DISCHARGE DOES NOT CAUSE OR CONTRIBUTE TO A VIOLATION OF WATER QUALITY STANDARDS. THE ALLOWABLE NON-STORMWATER DISCHARGES THAT OCCUR DURING CONSTRUCTION ON THIS PROJECT ARE LISTED IN PART 3.2 OF THE GENERIC PERMIT AS FOLLOWS:
- DISCHARGES FROM FIRE FIGHTING ACTIVITIES
- FIRE HYDRANT FLUSHINGS
- WASHWATERS WITH OUT DETERGENTS USED TO SPRAY OFF LOOSE SOLIDS FROM VEHICLES.
- DUST CONTROL PER PERMIT REQUIREMENTS
- POTABLE WATER SOURCES SUCH AS WATERLINE FLUSHINGS.
- LANDSCAPE IRRIGATION AND DRAINAGE.
- ROUTINE EXTERNAL BUILDING WASHDOWN PROVIDED NO DETERGENTS ARE USED.
- PAVEMENT WASHWATERS THAT DO NOT CONTAIN DETERGENTS, LEAKS, SPILLS OF TOXIC OR HAZARDOUS MATERIALS.
- AIR CONDITIONING CONDENSATE.
- SPRING WATER
- FOUNDATION OR FOOTING DRAIN FLOWS THAT ARE NOT CONTAMINATED WITH PROCESS MATERIAL SUCH AS SOLVENTS.
- NON-CONTAMINATED GROUND WATER ASSOCIATED WITH DEWATERING ACTIVITIES AS DESCRIBED IN PART 3.4 OF THE GENERIC PERMIT.



PLAN VIEW



SECTION A - A

NOTES:
1. DROP INLET SEDIMENT BARRIERS ARE TO BE USED FOR SMALL, NEARLY LEVEL DRAINAGE AREAS. (LESS THAN 5%).
2. THE TOP OF THE FRAME (PONDING HEIGHT) MUST BE WELL BELOW THE GROUND ELEVATION DOWNSLOPE TO PREVENT RUNOFF FROM BYPASSING THE INLET. A TEMPORARY DIKE MAY BE NECESSARY ON THE DOWNSLOPE SIDE OF THE STRUCTURE.
3. FASTEN FRAMING TO STRUCTURE TO ALLOW GRATE REMOVAL.
4. LEAVE EXPOSED EDGE TO ALLOW FOR PAVING TO GRADE

FILTER FABRIC INLET PROTECTION DETAIL

N.T.S.

NOTE:
AVOID USING IN TRAFFIC AREAS AS THIS CAN CAUSE A HAZARD.

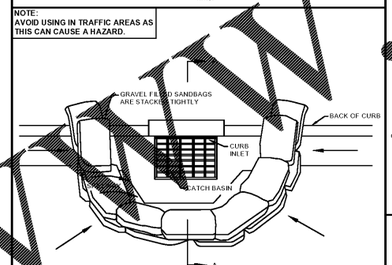

PLAN VIEW



SECTION A-A

NOTES:
1. PLACE CURB TYPE SEDIMENT BARRIERS ON GENTLY SLOPING STREET SEGMENTS WHERE WATER CAN POND AND ALLOW SEDIMENT TO SEPARATE FROM RUNOFF.
2. SANDBAGS OF EITHER BURLAP OR WOVEN GEOTEXTILE FABRIC, ARE FILLED WITH GRAVEL, LAYERED AND PACKED TIGHTLY.
3. LEAVE ONE SANDBAG GAP IN THE TOP ROW TO PROVIDE A SPILLWAY FOR OVERFLOW.
4. INSPECT BARRIERS AND REMOVE SEDIMENT AS NECESSARY. SEDIMENT AND GRAVEL MUST BE REMOVED FROM THE TRAVELED WAY IMMEDIATELY.

CURB INLET PROTECTION DETAIL

N.T.S.

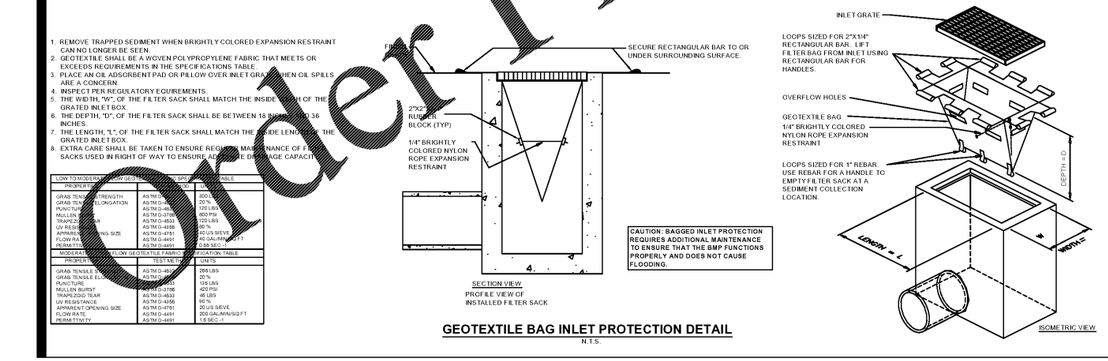

1. REMOVE TRAPPED SEDIMENT WHEN BRIGHTLY COLORED EXPANSION RESTRAINT CAN NO LONGER BE SEEN.
2. GEOTEXTILE SHALL BE A WOVEN POLYPROPYLENE FABRIC THAT MEETS OR EXCEEDS REQUIREMENTS IN THE SPECIFICATIONS TABLE.
3. PLACE AN OIL ADSORBENT PAD OR PILLOW OVER INLET GRATE WHEN OIL SPILLS ARE A CONCERN.
4. INSPECT PER REGULATORY EQUIREMENTS.
5. THE WIDTH, "W", OF THE FILTER SACK SHALL MATCH THE INSIDE WIDTH OF THE GRATED INLET BOX.
6. THE DEPTH, "D", OF THE FILTER SACK SHALL BE BETWEEN 18 AND 36 INCHES.
7. THE LENGTH, "L", OF THE FILTER SACK SHALL MATCH THE INSIDE LENGTH OF THE GRATED INLET BOX.
8. EXTRA CARE SHALL BE TAKEN TO ENSURE REGULAR MAINTENANCE OF FILTER SACKS USED IN RIGHT OF WAY TO ENSURE ADEQUATE DRAINAGE CAPACITY.

CAUTION: BAGGED INLET PROTECTION REQUIRES ADDITIONAL MAINTENANCE TO ENSURE THAT THE BMP FUNCTIONS PROPERLY AND DOES NOT CAUSE FLOODING.

LOW TO MODERATE FLOW GEOTEXTILE FABRIC SPECIFICATION TABLE

PROPERTY	TEST METHOD	UNITS
GRAB TENSILE STRENGTH	ASTM D-4632	200 LBS
GRAB TENSILE ELONGATION	ASTM D-4632	20%
PUNCTURE	ASTM D-4833	120 LBS
MULLEN BURST	ASTM D-3786	600 PSI
TRAPEZOID TEAR	ASTM D-4533	100 LBS
UV RESISTANCE	ASTM D-4355	90 %
APPARENT OPENING SIZE	ASTM D-4751	#50 U.S. SIEVE
FLOW RATE	ASTM D-4491	40 GAL/MIN/SQ FT
PERMITTIVITY	ASTM D-4491	0.55 SEC-1

MODERATE FLOW GEOTEXTILE FABRIC SPECIFICATION TABLE

PROPERTY	TEST METHOD	UNITS
GRAB TENSILE STRENGTH	ASTM D-4632	250 LBS
GRAB TENSILE ELONGATION	ASTM D-4632	30
